



Montgomery County Government • Department of Transportation

2013

Restoring Neighborhood Infrastructure

Progress Report through June 2013



RENEW MONTGOMERY

RENEW MONTGOMERY

Restoring Neighborhood Infrastructure

Renew Montgomery is a comprehensive program which coordinates Department of Transportation services to improve the infrastructure of mature neighborhoods. The program helps to assure safe and attractive access to business districts, public facilities, and recreational opportunities. It also serves to enhance neighborhoods, ensuring a high quality of life in the County.

"The Renew Montgomery program has had several positive impacts on my neighborhood. First, badly needed infrastructure improvements were made. Second, the neighborhood is safer and looks cleaner. Third, the improvements have left a positive image of County government on many of the neighbors. They can see that a significant amount of attention was paid to the area."

*Philip Olivetti, President
Linden Civic Association
Silver Spring, Maryland*

"On behalf of the Connecticut Avenue Estates Civic Association, I want to thank your department for the great work that was done upgrading specified sidewalks, gutters and curbs with ADA enhancements, and repaving CAE's streets. It was interesting watching the workers in action and the displaying of teamwork with the various 'Mighty Machines' from surveying up to the final laying out of . . . the hot mix asphalt. There was good coordination between the D.O.T. and others in the area . . . CAE neighbors took advantage of getting a lead and apron for their driveways which helped some of the parking problems that we have here. This Renew Montgomery program adds to the beautification for the County and should increase the property value of our 600-plus homes. Thank you."

*Carolyn Gupta, President
Connecticut Avenue Estates Civic Association
Silver Spring, Maryland*

This report was prepared by the Community Outreach program within the Director's Office of the Department of Transportation. For questions about *Renew Montgomery* or for additional copies of this report, call 240.777.7155 or write to the above office at 101 Monroe Street, 10th Floor Rockville, Maryland 20850-2540 or mcdot.outreach@montgomerycountymd.gov.

TABLE OF CONTENTS

INTRODUCTION.....	1
SERVICES PROVIDED.....	2
STATUS OF RENEW MONTGOMERY NEIGHBORHOODS	4
EXPENDITURES BY FISCAL YEAR.....	20
SAMPLE LETTER FROM CIVIC ASSOCIATION OFFICIAL IDENTIFYING NEIGHBORHOOD ISSUES	21
MAPS OF FY02 RENEW MONTGOMERY NEIGHBORHOODS	22
Hillandale Heights	
Stratton Woods/Marymount	
Westgate/Crestview/Westhaven	
MAPS OF FY03 RENEW MONTGOMERY NEIGHBORHOODS	26
Calverton	
Hillandale	
Homewood/Capital View Park	
North Bethesda Grove	
Woodmoor/Indian Spring Village	
MAPS OF FY04 RENEW MONTGOMERY NEIGHBORHOODS	32
Merrimac Park/Woodburn	
Woodside Park East	
MAPS OF FY05 RENEW MONTGOMERY NEIGHBORHOODS	35
Brookdale/Green Acres/Glen Cove	
Glenview	
Northwood Park	
Sumner	
Wyngate/Ashburton/Alta Vista Terrace	
MAPS OF FY06 RENEW MONTGOMERY NEIGHBORHOODS	41
Glenwood/Glenbrook Knolls	
South Four Corners	
Wohlshire	
MAPS OF FY07 RENEW MONTGOMERY NEIGHBORHOODS	45
Carroll Knolls/Plyers Mill Estates/Oakland Terrace	
Sligo Park Knolls/Oranges/Breewood Manor	
Westmoreland Hills	
MAPS OF FY08 RENEW MONTGOMERY NEIGHBORHOODS	49
Garrett Park	
Greenwood Knolls	
MAPS OF FY09 RENEW MONTGOMERY NEIGHBORHOODS	52
Wheaton Woods	
MAPS OF FY12 RENEW MONTGOMERY NEIGHBORHOODS	54
Kingswell/Glenmont Forest	
CONCLUSION	56

RENEW MONTGOMERY PROGRESS REPORT

INTRODUCTION

The Montgomery County Department of Transportation periodically publishes a progress report on the *Renew Montgomery* program. This report contains background information on the program, listing of participating neighborhoods, financial summaries, and maps of designated and still active *Renew Montgomery* neighborhoods since fiscal year 2003. In addition the report contains construction updates available when reprinting occurred.

Renew Montgomery continues to be successful in addressing the infrastructure needs of the County. Since its beginning in 1997, *Renew Montgomery* has improved or is programmed to improve infrastructure conditions in 72 areas of the county (through FY13) at an investment of \$68 million (expenditures through the close of FY12).



SERVICES PROVIDED

Renew Montgomery continues to coordinate Montgomery County Department of Transportation (MCDOT) services where appropriate and as determined by departmental guidelines. These services may include:

AMERICAN WITH DISABILITIES ACT (ADA) IMPROVEMENTS

Provision of accessible streets, roads, and walkways for people with disabilities by installing curb ramps; removing barriers on existing sidewalks, such as signs, poles, and fences, which hamper accessibility to wheelchair users; and reconstructing median breaks and sidewalks to comply with the ADA. For information on these types of improvements in your neighborhood, installed by the Division of Transportation Engineering, call 311.

BUS STOP AMENITIES

Installation of Ride On bus stop signs, shelters, benches and bus stop access improvements such as connecting sidewalks and waiting pads where applicable. For information on these types of improvements in your neighborhood, installed by the Division of Transit Services, call 311.

NEIGHBORHOOD BEAUTIFICATION

Designation of beautification grants to assist neighborhoods with beautification projects. Through the *Keep Montgomery County Beautiful* program, neighborhoods are eligible for a grant of up to \$500 to match the community's share of a beautification project. Note, these grants are temporarily suspended due to fiscal constraints. Types of projects can include planting flowers, shrubs, or trees; landscaping a community entranceway; converting weed fields to grassy areas; and planting rain gardens. For information on these grants for your neighborhood, contact MCDOT Community Outreach, at 240.777.7155.

ROADWAY BASE REPAIRS

Removal and replacement of defective road base which allows water penetration and the resulting road failures. This work is completed prior to sealing/resurfacing roads. For information on work underway in your neighborhood, handled by the Division of Highway Services, call 311.

ROAD RESURFACING

Application of a durable surface which offers improved traction and coloration to road surfaces. For information on work underway in your neighborhood, handled by the Division of Highway Services, call 311.

SIDEWALK, CURB AND GUTTER REPAIR

Removal and replacement, in kind, those public sidewalks, curbs and gutters which are cracked, raised, exhibit periodic ponding or have missing segments. For information on work underway in your neighborhood, handled by the Division of Highway Services, call 311.

SIDEWALKS - NEW

Construction of sidewalks to encourage greater pedestrian circulation throughout neighborhoods and to provide safe access to schools, transit facilities, parks, and other major pedestrian destinations. Requests for construction are prompted by members of the community seeking improved pedestrian access. For information on these types of improvements in your neighborhood, installed by the Division of Transportation Engineering, call 311.

SIGN AND MARKING MAINTENANCE

Removal, repair or replacement of damaged, vandalized or faded traffic signs and pavement markings. For information on these types of improvements in your neighborhood, installed by the Division of Traffic Engineering and Operations, call 311.

STORM DRAIN IMPROVEMENTS

Analysis and design to upgrade substandard existing systems in conjunction with sidewalk, curb and gutter replacement and resurfacing. Provision of new drainage structures where possible to improve chronic problems. Identification of major system improvements for future Capital Projects when warranted. For information on these types of improvements in your neighborhood, installed by the Division of Transportation Engineering, call 311.

STREET LIGHTING

At the request of a two-thirds majority of effected residents, areas that have substandard lighting are identified. Street lighting improvements (i.e. upgrade of existing or installation of new streetlights) are designed then implemented to achieve lighting levels that meet County standards. For information on these types of improvements in your neighborhood, installed by the Division of Traffic Engineering and Operations, call 311.

TRAFFIC CALMING

Identification of residential streets which would benefit from installation of various modifications to the roadway as warranted by engineering standards and supported by the community. These measures reduce the negative effects of motor vehicle use such as speeding and neighborhood cut-through traffic, alter driver behavior, and improve conditions for pedestrians. For information on proposing these measures for your neighborhood, installed by the Division of Traffic Engineering and Operations, call 311.

TREE MAINTENANCE

Resolution of priority and requested tree maintenance needs. Work may include tree and stump removal of appropriate trees, pruning to resolve pending priority citizen requests, and replacement tree planting. For information on work underway in your neighborhood, handled by the Division of Highway Services, call 311.

The following table lists all of the neighborhoods currently in the program and provides an indication of their status. The table lists the neighborhoods in alphabetical order to aid in locating a specific community. The various refurbishment updates are grouped by the type of work done within each community.

TABLE 1
RENEW MONTGOMERY NEIGHBORHOODS SORTED BY COMMUNITY NAME
 Effective May 20, 2013

Neighborhood	FY YR Selected	Treatment	Status	Comments
Alta Vista Terrace	FY 05	Other	Started	* See Wyngate listing
Alta Vista/Maplewood	FY 00	Concrete Construction	Complete	* Concrete curb and gutter work complete. (Rpaugh, fall, 2010?)
Alta Vista/Maplewood	FY 00	Drainage Improvements	Complete	* Drainage system refurbishments were made on [Beech Avenue] under Drainage assistance request program. (YA, 6/11/07)
Alta Vista/Maplewood	FY 00	Other	Complete	Renew Montgomery work now finished. Close out letter TP office for review RP 3/15/11
Alta Vista/Maplewood	FY 00	Resurfacing	Complete	* Resurfacing was completed by July, 2010. (Rpaugh 2/7/11)
Alta Vista/Maplewood	FY 00	Traffic Engineering	Complete	* 7 streetlights to be installed along Beech Av. (MC, 2/6/06)
Ashburton	FY 05	Other	Started	* See Wyngate listing
Bannockburn	FY 97	Other	Complete	* Renew Montgomery work completed.
Battery Park	FY 00	Other	Complete	* See Greenwich Forest listing.
Bel Pre Woods	FY 98	Other	Complete	* Letter from County Executive to civic leaders sent. (TP, 1/04) * Contact proved invalid. (TP, 2/04)
Bradley Park	FY 03	Other	Started	* See Woodhaven/Highland Hills listing.
Breewood Manor	FY 07	Other	Started	* See Sligo Park Knolls
Brookdale/Green Acres/Glen Cove	FY 05	Concrete Construction	Complete	* Concrete curb & gutter work has been started, with installations in Green Acres now complete. The remainder should be completed by next construction season, starting in late summer of 2006. (JB to L.Howe per LH, 2/2/05) * Curb & gutter refurbishment now complete in the Glen Cove neighborhood. (JB, 8/7/2006) * Highway Services received a signed petition in 11/05 from Mr. Larry Howe, Public Works Coordinator, of the Brookdale Citizens Association. That petition contained the 80% (75 of 93) homeowners signing to add concrete curbing on multiple streets in the Brookdale/ Wohlshire area. We have scheduled the curb installations to begin in this Renew Montgomery area in the July / August timeframe. (JB, 5/5/08) * Glen Cove Road was scheduled for special concrete work in late summer, '08. (JB, 8/11/08) * Concrete work completed (AD, 7/16/07). * However, additional work needed on an area in the south of the neighborhood. (JB, 11/7/11)
Brookdale/Green Acres/Glen Cove	FY 05	Drainage Improvements	Complete	* We just completed a storm drainage project on Baltimore Ave. and all concrete work is completed. (AD, 1/7/08) * Baltimore Ave. -- completed all storm drainage work. (1/7/08,AD)
Brookdale/Green Acres/Glen Cove	FY 05	Resurfacing	Started	* Highway Services waiting on its Road Condition Assessment to be completed before scheduling further resurfacing work. There is also additional curb & gutter work needed at intersection of Park Av & Keokuk St. (JB, 10/6/08). * Resurfacing of remaining streets needed--was accidentally overlooked. DHS expects to get to these in the spring 2012 construction season. (JB, 11/7/11)
Brookdale/Green Acres/Glen Cove	FY 05	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Brookdale/Green Acres/Glen Cove	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Brookdale/Green Acres/Glen Cove	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work (BL, 5/30/08)
Brookmont	FY 97	Other	Complete	* Renew Montgomery work completed.
Calverton	FY 03	Concrete Construction	Complete	* Concrete work, including extensive Gracefield Road work, completed by 10/04. (JB, 1/10/05)
Calverton	FY 03	Drainage Improvements	Unknown	* None
Calverton	FY 03	Other	Started	Renew Montgomery work now finished. Close out letter TP office for review RP 3/15/11

Calverton	FY 03	Resurfacing	Complete	* Resurfacing of Calverton Road between Cherry Hill Rd and the county line scheduled to begin in May, 09. (RP, 5/4/2009) * Resurfacing underway as of 7/30/10 (JB 8/5/10) * Resurfacing completed. (RPaugh 12/1/20) * Ready for Close Out letter preparation? (TP, 12/5/10)
Calverton	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Calverton	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
Calverton	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Carderock Springs	FY 98	Other	Complete	* Renew Montgomery work completed.
Carroll Knolls	FY 98	Other	Complete	* Renew Montgomery work completed.
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Bus Stop Improvements	Complete	* Bus stop improvements—largely sidewalk connections—were made along Dexter Av, from Brunswick to Plyers Mill Rd. (LW, 11/3/08)
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Concrete Construction	Started	* New sidewalk connection installed at a cost of \$10,780 between Glenway/Pearson to McComus Av. (RE, 11/7/07) * Highway Maintenance installed a temporary patch on Pearson Street. This patch will hold up for about five to ten years, but will be replaced before that time frame. The curb and gutter will be installed properly and the road will be re-graded during the course of Renew Montgomery in this neighborhood. (AD, 10/29/07) * Highway Services intends to start curb & gutter work in this neighborhood sometime in September, 08 and should stay in the area until the end of October, 08. The neighborhood is slated for four years which means DHS won't complete the whole neighborhood this year. The area closest to University Blvd. (Md.193) is the starting point; they will work down to Plyers Mill Rd toward I-495. (AD, 6/16/08) * Highway Services sent out in mid-Oct '08 a newsletter informing community that curb & gutter concrete work will be starting. * Concrete work completed for the season, will start back up in the summer, 09. (AD, 11/24/08) * 10% of concrete work completed. (RP, 1/5/09) * DHS is planning to begin concrete repairs in Carroll Knolls around October this year. This proposed work is based on availability of project funding and contractor scheduling. Experiencing inclement weather. (RP, 6/30/09) * We are scheduled to commence concrete repairs in September. (JB 8/5/10) Adam Updated FY11\$ (8/31/11) Commenced repairs on 10/7/10. Contractor will finish the construction season in this area. (Rpaugh 12/1/10) * Concrete work 1% complete. (DHS construction report, 10/14/11) * Concrete work 75% complete. (DHS construction report 11/11/11) * Concrete work 90% complete. (per RP, 2/6/12) * Concrete work completed for season. (DHS Rpt, 7/6/12)**Kensington Hghts Concrete work 65% as of 7/6/12. (DHS By-Weekly Status Report 11/24/2012)
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Drainage Improvements	Complete	* Storm Drain/Curb install-Decatur Avenue- complete 4/16/12(DHS Bi-Weekly stats report 11/14/12)
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Other	Started	* Community Outreach Office sends to civic organization contact an introductory letter announcing neighborhood selection for Renew Montgomery program. (3/2/07) * Community Outreach Program Manager meets with community at June, 07 Carroll Knolls Civic Association meeting to brief on Renew Montgomery. (TP, 6/28/07) * Civic association president from Kensington Heights called to advise that at least a portion of his community is included in these boundaries—west end. Briefing scheduled for 10/2/07 association meeting. (Wayne Goldstein, 9/5/2007) * Civic association briefed on program in October, 07. (TP, 10/3/2007)
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Resurfacing	Complete	* Resurfacing was started 3/12/12. Currently 85% complete. (DHS bi-weekly rpt, 5/12/12)*Permanent patch work complete(DHS By-Weekly Report Stats 11/24/2012)
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Carroll Knolls/Plyers Mill	FY 07	Traffic	Complete	* Traffic Engineering reported replacing four street signs and poles (JP,

Ests./Oakland Terrace [includes Kensington Heights CA]		Engineering		10/1/07) * DTEO may do new crosswalk markings once resurfacing is complete. (JP, 2/6/12)
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Traffic Engineering	Started	<p>* The faded signs at the intersection of Findley Road and Devin Place have been replaced. The foliage obstructing stop signs at the intersections of McComas Avenue and Pearson Street and St. Paul Street and McComas Avenue has been trimmed back. An extended "No Parking Any Time" prohibition has been installed on Drumm Avenue at the intersection with University Boulevard. (JP, 5/12/09)</p> <p>* The Division of Traffic Engineering & Operations (DTEO) conducted studies at the intersections of McComas Avenue and Bentley Street and Drumm Avenue and Decatur Avenue based on requests for additional stop signs by residents. However it was determined that all-way stops were not warranted at these intersections. The stop sign on Bentley Street at McComas Avenue was replaced.</p> <p>* The request for a marked crosswalk to Kensington Heights Park at the intersection of McComas Avenue and Farragut Avenue cannot be considered as there is no sidewalk on the south side of McComas Avenue or on Farragut Avenue. If sidewalks were built at these locations, our department could re-examine this issue. (JP, 5/12/09)</p> <p>* All of the street light outages are on record as having been reported to DTEO; however, since most of them are maintained by PEPCO they do not receive reports of the work being completed. (JP, 5/12/09)</p> <p>* Regarding traffic calming requests, the results of the spot speed studies that we conducted for McComas Ave, Drumm Ave and Hobson Street indicated these streets did not meet DTEO's speed and volume criteria for speed humps. The prohibitively steep grades along the entirety of Drumm Ave and Hobson Street also were at issue, as well as the insufficient length of Faulkner Place (must be at least 1,000' long). Along a portion of McComas Ave, the grade is too steep to be suitable for placing speed humps. However, it appears that there are other locations that have acceptable grades and are located 500'-750' from other suitable locations, so that development of a viable speed hump layout would be possible for at least part of the street (if the speed and volume criteria were met). DTEO staff are going to re-check this street for speed and volumes. (TW, 5/13/09)</p>
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 for Carroll Knolls (BL, 8/28/08)
Carroll Knolls/Plyers Mill Ests./Oakland Terrace [includes Kensington Heights CA]	FY 07	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Chevy Chase Hills	FY 01	Concrete Construction	Complete	* Concrete completed. (2/20/09)
Chevy Chase Hills	FY 01	Drainage Improvements	Complete	* Concrete curb and gutter work complete.
Chevy Chase Hills	FY 01	Other	Complete	* Renew Montgomery work now finished. Letter from County Executive to civic leaders sent. (RP, 5/26/2009)
Chevy Chase Hills	FY 01	Resurfacing	Complete	* Final micro paving completed in 2003. (RP, 1/5/09) * Resurfacing completed. (2/20/09)
Chevy Chase Hills	FY 01	Traffic Engineering	Complete	* None
Chevy Chase West	FY 98	Other	Complete	* Renew Montgomery work completed.
College View	FY 02	Concrete Construction	Complete	* None
College View	FY 02	Drainage Improvements	Complete	* None
College View	FY 02	Other	Complete	* Letter from County Executive to civic leaders sent. (ML, 3/7/2008)
College View	FY 02	Resurfacing	Complete	* Concrete work completed by 10/04. (DS, 11/1/04). * Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work. (AD, 1/25/08)
College View	FY 02	Resurfacing	Complete	* Final micro paving completed in FY04. (GL, 3/19/08)
College View	FY 02	Traffic Engineering	Complete	* Sign and marking. (JP, 2/19/08)
Connecticut Avenue Estates	FY 08	Concrete	Started	* Curb & gutter work projected to start this Spring. (RP, 10/5/09)

		Construction		Concrete work began on 7/6/10. We will attempt to complete all concrete work this construction season. (JB 8/5/10) * Concrete work has concluded for the season on 10/5/10. We'll be back to finish in Summer 2011. (RPaugh 12/1/20) * Newsletter sent out to community to advise of impending concrete work. (4/14/11) * Concrete work starts in May. (CAO report, 5/18/11) * Concrete work 85% complete. (DHS construction report, 6/11/11) Adam Updated FY11\$ (8/31/11) Concrete work 100% complete (DHS construction report 11/11/11)
Connecticut Avenue Estates	FY 09	Drainage Improvements	Unknown	* None
Connecticut Avenue Estates	FY 97	Other	Complete	* Renew Montgomery work completed. Ready for preparation of CE close out letter. (TP, 1/2012) Close out letters in TP's office for review (RP 4/17/12)
Connecticut Avenue Estates	FY 09	Other	In progress	* The Connecticut Avenue Estates area is a neighborhood where DHCA has made significant investment over many years. DHCA in partnership with Montgomery Housing Partnership (MHP) provided funding for single family rehab and public space improvements several years ago. Currently, we have a non-profit (MHP) under contract to provide outreach. This involves working with the Civic Association advertising and marketing meetings, coaching and occasional problem solving. If you need assistance in outreach to this neighborhood, please, let us know. (R. Roberts, 2/18/09) * Community Outreach Office sent to civic organization contacts introductory letter announcing neighborhood selection for Renew Montgomery program. (3/10/09) * Community Outreach Office agrees to sponsor under its pedestrian safety program in the amount of \$650 a community movie. This came as a result of a request from Carolyn Gupta, president of the Connecticut Avenue Estates Civic Association. August, 2011 civic association president requests MCDOT sponsorship of community outdoor movie. Presentation will in part promote traffic and pedestrian safety through public service announcements. President will also mention Renew Montgomery program. MCDOT provides \$666.00 sponsorship to fund rental of projector, screen, sound mixer, and speakers. Movie was shown on a Saturday evening in mid-September, 2011. (TP, 10/2011)
Connecticut Avenue Estates	FY 09	Resurfacing	Started	* Highway Maintenance has scheduled this neighborhood for resurfacing work on its FY13 schedule. (JB, 8/5/10) * Newsletter sent out to community to advise of impending resurfacing work. (6/10/11) * Started patching Nick Boone (6/20/11) * Adam D. added FY11 \$ (8/31/11) * Resurfacing work 80% complete within FY12 summer-fall construction season. (DHS construction report, 10/14/11) 95% complete. (DHS construction report, 11/11/11)
Connecticut Avenue Estates	FY 09	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10) * Streetlight unit installed in FY09 1 – 70 W, HPS Streetlight on Valleywood Drive(TS, 1/4/10)
Connecticut Avenue Estates	FY 09	Tree Maintenance and/or Replanting	Unknown	* None
Crestview	FY 02	Other	Started	* See Westgate listing
East Bethesda	FY 97	Other	Complete	* Renew Montgomery work completed.
East Silver Spring	FY 97	Other	Complete	* Renew Montgomery work completed.
East Springbrook	FY 02	Concrete Construction	Complete	* Concrete work completed. (DS, 7/12/04)
East Springbrook	FY 02	Drainage Improvements	Complete	* None
East Springbrook	FY 02	Other	Complete	* Renew Montgomery work now finished. * Letter from County Executive to civic leaders sent. (TP, 5/2006)
East Springbrook	FY 02	Resurfacing	Complete	* Final surface repairs, preparation, and resurfacing of roads completed. (GL, 12/12/05)
East Springbrook	FY 02	Traffic Engineering	Complete	* None
Edgemoor/Bradley Hills	FY 00	Other	Complete	* Renew Montgomery work now finished.
Edgemoor/Bradley Hills	FY 00	Resurfacing	Complete	* Resurfacing completed in 2007 (JB, 2/2/09)

Fairview Estates	FY 03	Concrete Construction	Complete	* Concrete work completed in 10/03. (DS, 10/13/03) * Concrete completed. (2/20/09)
Fairview Estates	FY 03	Other	Complete	* Renew Montgomery work now finished. * Letter from County Executive to civic leaders sent. (RP, 5/26/2009)
Fairview Estates	FY 03	Resurfacing	Complete	* Final micro paving completed. (RP, 1/5/09) * Resurfacing completed . (2/20/09)
Fairview Estates	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Fairview Estates	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08. (BL, 8/28/08)
Fairview Estates	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Four Corners	FY 98	Other	Complete	* Renew Montgomery work completed.
Garrett Park	FY 08	Concrete Construction	Complete	* Curb & gutter work projected to start in spring, 09. (RP, 1/5/09) * DHS will begin concrete work in July 09 and plans to complete half of the neighborhood within 2 months. Around June the community will receive a newsletter from DHS explaining the construction process and contact information. (AD, 5/5/2009) * HWS sends newsletter to residents advising of concrete repairs coming soon to their neighborhood (7/12/10 RP) * This season's concrete work started on 7/8/10. (JB 8/5/10) * Completed concrete repairs on 11/5/10. (Rpaugh 12/1/20) * Now ready for resurfacing of roads to complete Renew Montgomery work. Adam Updated FY11\$ (8/31/11)
Garrett Park	FY 08	Drainage Improvements	Unknown	* None
Garrett Park	FY 08	Other	Complete	* Programmed (2/08) * Community Outreach Office sends to Mayor of Town of Garrett Park & to civic organization contacts an introductory letter announcing neighborhood selection for Renew Montgomery program. (3/21/08)
Garrett Park	FY 08	Resurfacing	Complete	*Permanent patching work completed,by 10/22/2012. (DHS By-Weekly Status Report 11/24/2012)
Garrett Park	FY 08	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Glen Cove	FY 05	Other	Started	* See Brookdale listing.
Glen Echo Heights	FY 99	Other	Complete	* Renew Montgomery work completed.
Glenmont Forest/Kingswell	FY 12	Concrete Construction	Started	* 3/6/12 - Concrete repairs are planned for the fall. Due to the size of the area, this will probably be a two or three construction season project. After completion of the concrete repairs, we will be performing roadway patching on the entire neighborhood in anticipation of resurfacing taking place soon thereafter. Newsletters will be sent out to entire area 3-4 weeks prior to work commencing. J Birton/RP. 10/22/12 Concrete repairs are 100% for this season. We will finish all concrete repairs next season. The current scheduled start for resurfacing is FY20. (John Birton/R2P, 11/2/12)
Glenmont Forest/Kingswell	FY 12	Drainage Improvements	Not Started	* None
Glenmont Forest/Kingswell	FY 12	Other	Started	* Bus shelter on SB Georgia Ave at the interestecion with Weisman Rd was relocated in the summer of 2011. New Ride On Route 58 was started along Judson. New bus stop signs and pads to follow. (L. Winestone, 3/11/2013)
Glenmont Forest/Kingswell	FY 12	Resurfacing	Started	*Permanent patching 65%(DHS by weekly stats report 11/24/2012)
Glenmont Forest/Kingswell	FY 12	Traffic Engineering	Started	2/6/2013 - Discussions underway with Civic President, Mr. Jardaneh, regarding traffic calming measures on selected streets. Traffic engineer (Seifu Kerse) also evaluating other engineering requests contained in updated 2013 neighborhood issues list. (T.Wroe, 2/6/2013 email)

Glenview	FY 05	Concrete Construction	Complete	<ul style="list-style-type: none"> * Concrete curb & gutter work has been started, with approximately 45% of the work installed. (JB, 8/8/05) * Highway Maintenance will try to finish this area in FY07 but if it takes more than 3 months they must move on and come back to the area in 08 (sidewalk and curb work is about 75% done). (AD, 12/4/06) * Concrete work will be about 85% completed at the end of July 2007 and will finish in FY08. (AD, 7/16/07) All concrete work is done for this year. (AD, 10/1/07) * We will return to this area in FY09 to complete the final stage of concrete work. (AD, 1/7/08) * Concrete work stopped for the season, will start back up in the summer, 09. (AD, 11/24/08) * Curb & gutter work 90% complete. (RP, 1/5/09) * Completed(AD 7/17/09)
Glenview	FY 05	Drainage Improvements	Complete	* Drainage system refurbishments were made on Glen Haven Drive under the Drainage Assistance Request Program in the amount of (YA, 6/11/07)
Glenview	FY 05	Other	Started	* Department of Environmental Protection conducting outreach to the community on its Rainscaping Program. (JB, 10/6/08)
Glenview	FY 05	Resurfacing	Started	<ul style="list-style-type: none"> * Mainline overlay on Inwood Avenue (DN, 7/16/07) * Neighborhood streets resurfacing programmed for FY10. Work should begin in summer, 09. (RP, 5/4/2009) * Highway Maintenance has scheduled this neighborhood for hot mix asphalt resurfacing work on its FY10 schedule. (JB, 7/16/09)
Glenview	FY 05	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Glenview	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Glenview	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance unit work (BL, 7/3/08)
Glenwood/Glenbrook Knolls	FY 06	Concrete Construction	Complete	<ul style="list-style-type: none"> * Concrete work to start in Oct, 2007. (AD, 10/1/07) * All concrete curb & gutter work is completed in this community. (AD, 2/18/09)
Glenwood/Glenbrook Knolls	FY 06	Drainage Improvements	Complete	* The cost for the new storm drainage project at 8511 Hazelwood Drive (YA, 12/5/08)
Glenwood/Glenbrook Knolls	FY 06	Resurfacing	Started	* Note that slurry sealing was done on streets in Glenwood in FY03. (GL, 12/12/05)
Glenwood/Glenbrook Knolls	FY 06	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Good Hope Estates	FY 04	Concrete Construction	Complete	* New sidewalk installed on Keystone Av from N Brooke La to Battery La (\$21,129) by Division of Transportation Engineering (RE, 2/9/12 spreadsheet).
Good Hope Estates	FY 04	Drainage Improvements	Complete	* Repairs to existing concrete curb and gutters completed by 9/04. (JB, 1/10/05) (AD, 2/28/08).
Good Hope Estates	FY 04	Other	Complete	* Letter from County Executive to civic leaders sent. (ML, 3/7/2008)
Good Hope Estates	FY 04	Resurfacing	Complete	* Roads resurfaced. (Date NA)
Good Hope Estates	FY 04	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Good Hope Estates	FY 04	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance unit work done for FY09 (per BL email 1/15/10)
Good Hope Estates	FY 04	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
Green Acres	FY 05	Other	Started	* See Brookdale listing
Greenwich Forest/Battery Park	FY 00	Concrete Construction	Complete	<ul style="list-style-type: none"> * Highway Maintenance considering proposing a Capital Improvement Program project that would fund completely rebuilding the streets in this neighborhood. The concrete base of most of the roads has seriously deteriorated. (J.Hawkes, 3/6/06) * Concrete completed. (2/20/09)
Greenwich Forest/Battery Park	FY 00	Drainage Improvements	Complete	<ul style="list-style-type: none"> * Awaiting storm drainage work (em to J.Hawkes for update, 3/3/06). * Storm drain work has been completed. (JB, 8/6/07)
Greenwich Forest/Battery Park	FY 00	Other	Complete	* Renew Montgomery work now finished. * Letter from County Executive to civic leaders sent. (RP, 5/26/2009)
Greenwich Forest/Battery Park	FY 00	Resurfacing	Complete	* Road repair on Battery Park and Maple Ridge done. (GL, 12/12/05)

				<p>* Road work to be scheduled next construction season. (JB, 8/6/07)</p> <p>* Division of Highway Services announces new Paving Initiative that will start with an \$850,000 investment in Battery Park. Refurbishment of roads and sidewalks along with block pruning of trees will begin in July, 2008 and be completed by the fall. Contact Frank Kingsley for details. See County Press Release dated 7/23/08.</p> <p>* Neighborhood pavement refurbishment completed. See County Press Release dated 12/17/08. Resurfacing completed . (2/20/09)</p>
Greenwich Forest/Battery Park	FY 00	Traffic Engineering	Complete	* None
Greenwich Forest/Battery Park	FY 00	Tree Maintenance and/or Replanting	Complete	* Tree maintenance work. (BL, 3/4/09)
Greenwood Knolls	FY 08	Concrete Construction	Complete	<p>** Curb & gutter work projected to start this construction season, 09. (JB, 7/16/09) * We were not able to do any work in this area due to budget. We'll return in the Summer/Fall 2011. (RPaugh 12/1/20) * Concrete work scheduled for spring-summer construction season. (DHS construction report, 6/11/11) * Newsletter sent to community. (6/1/11) * Adam D. added FY11 \$ (8/31/11) * Concrete work 100% complete. (DHS construction report, 10/14/11) – but per JB, there is another 2% of work needed due to WSSC work. DHS must go back and do some restoration work. (11/7/11) Concrete work 100% complete. (DHS construction report 10/14/11)</p>
Greenwood Knolls	FY 08	Drainage Improvements	Unknown	* None
Greenwood Knolls	FY 08	Other	Complete	* Community Outreach Office sends to civic organization contact an introductory letter announcing neighborhood selection for Renew Montgomery program. (3/21/08)
Greenwood Knolls	FY 08	Resurfacing	Started	*Permanent patching70%- (DHS by weekly stat report 11/24/2012)
Greenwood Knolls	FY 08	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Heritage Walk	FY 03	Other	Complete	* See Luxmanor listing.
Highland View	FY 01	Concrete Construction	Complete	* Concrete curb and gutter work complete.
Highland View	FY 01	Drainage Improvements	Complete	* None
Highland View	FY 01	Other	Complete	* Letter from County Executive to civic leaders sent. (ML, 3/7/2008)
Highland View	FY 01	Resurfacing	Complete	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work (AD, 1/25/08)
Highland View	FY 01	Traffic Engineering	Complete	* Final micro paving completed. (GL, 11/5/07)
Highland View	FY 01	Traffic Engineering	Complete	* Sign and marking. (JP, 2/19/08)
Hillandale (East of NH Av)	FY 03	Concrete Construction	Unknown	* None
Hillandale (East of NH Av)	FY 03	Drainage Improvements	Complete	* Sweetbriar Storm Drain project was completed in the summer, 04. (JM, 6/7/04)
Hillandale (East of NH Av)	FY 03	Resurfacing	Not Started	* Curb and gutter work complete by 8/04. (DS, 9/13/04)
Hillandale (East of NH Av)	FY 03	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Hillandale (East of NH Av)	FY 03	Traffic Engineering	Unknown	* None
Hillandale (East of NH Av)	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Hillandale (East of NH Av)	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
Hillandale Heights	FY 02	Concrete Construction	Complete	* Concrete work completed by 9/04 (DS, 11/1/04).
Hillandale Heights	FY 02	Drainage Improvements	Unknown	* None
Hillandale Heights	FY 02	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Hillandale Heights	FY 02	Traffic Engineering	Unknown	* None
Hollyoak	FY 03	Other	Complete	* See Luxmanor listing.

Homewood/Capital View Park	FY 03	Concrete Construction	Complete	* Additional investment. (AD 7/17/09)
Homewood/Capital View Park	FY 03	Concrete Construction	Complete	* Curb and gutter work 99% complete. Final work on hold pending WSSC work. (JB, 6/6/05) WSSC did work in one neighborhood which held up the curb & gutter work and resurfacing. (YA, 6/11/07) * WSSC work completed; curb & gutter work will be restarted next spring. (AD, 7/16/07) * This area will be reentered in FY09 to complete the rest of the concrete work missed due to WSSC. (AD, 1/7/08) * Curb & gutter work 95% complete. Just a couple of streets remain. (RP, 1/5/09) * All concrete work is completed. (AD, 7/17/2009)
Homewood/Capital View Park	FY 03	Drainage Improvements	Unknown	* None
Homewood/Capital View Park	FY 03	Resurfacing	Started	* Slurry seal 85% complete. Drum Av will be scheduled for microseal hopefully in the 2006 construction season. (GL, 4/10/06)
Homewood/Capital View Park	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09. (JP1/25/10)
Homewood/Capital View Park	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Homewood/Capital View Park	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 for Homewood (BL, 8/28/08)
Indian Spring Terrace	FY 02	Concrete Construction	Complete	* Concrete completed (DS, 11/1/04).
Indian Spring Terrace	FY 02	Drainage Improvements	Unknown	* None
Indian Spring Terrace	FY 02	Other	Complete	Renew Montgomery work now finished. Close out letter in TP's office waiting on approval then will send to CE. (RP 4/22/13) Letter to Walter Gottlieb and Tony Hausner
Indian Spring Terrace	FY 02	Resurfacing	Complete	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work. ** Highway Services sends newsletter to residents in this designated Renew Montgomery community advising of resurfacing work coming soon (on or about 5/28/10) to their neighborhood. (5/20/10) * Neighborhood Resurfacing is Complete. (JB 8/5/10)
Indian Spring Terrace	FY 02	Traffic Engineering	Unknown	* None
Indian Spring Village	FY 03	Other	Started	* See Woodmoor listing.
Kemp Mill Estates/Farms	FY 99	Other	Complete	* Renew Montgomery work completed.
Kensington Heights	FY 07	NA	NA	* See Carroll Knowles
Kenwood	FY 02	Concrete Construction	Complete	* Concrete work completed in 10/02.
Kenwood	FY 02	Drainage Improvements	Complete	* None
Kenwood	FY 02	Other	Complete	* Letter from County Executive to civic leaders sent 11/3/05.
Kenwood	FY 02	Resurfacing	Complete	* Slurry sealing completed fall, 04. (GL, 6/6/05)
Kenwood	FY 02	Traffic Engineering	Complete	* None
Kingswell	FY 12	NA	NA	* See Glenmont Forest
Linden	FY 03	Other	Complete	* See Montgomery Hills listing.
Locust Hill	FY 01	Concrete Construction	Complete	* Concrete curb and gutter work complete.
Locust Hill	FY 01	Drainage Improvements	Complete	* None
Locust Hill	FY 01	Other	Complete	* Letter from County Executive to civic leaders sent. (ML, 3/7/2008)
Locust Hill	FY 01	Resurfacing	Complete	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work. (AD, 1/25/08) * Final micro paving completed. (GL, 11/5/07)
Locust Hill	FY 01	Traffic Engineering	Complete	* Sign and marking. (JP, 2/19/08)
Longbranch	FY 97	Other	Complete	* Renew Montgomery work completed.
Luxmanor/Hollyoak/Heritage Walk	FY 03	Concrete Construction	Complete	* Concrete work completed by 9/04. (DS, 9/13/04) * Concrete completed . (2/20/09)

Luxmanor/Hollyoak/Heritage Walk	FY 03	Drainage Improvements	Complete	* Drainage system refurbishments were made on Hunt Over Lane under the Drainage Assistance Program (YA, 6/11/07)
Luxmanor/Hollyoak/Heritage Walk	FY 03	Other	Complete	* Renew Montgomery work now finished. Letter from County Executive to civic leaders sent. (RP, 5/26/2009)
Luxmanor/Hollyoak/Heritage Walk	FY 03	Resurfacing	Complete	* Final micro paving completed in 2001. (RP, 1/5/09) * Resurfacing completed . (2/20/09)
Luxmanor/Hollyoak/Heritage Walk	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Luxmanor/Hollyoak/Heritage Walk	FY 03	Tree Maintenance and/or Replanting	Complete	*Tree Maintenance work done for FY09 (per BL email 1/15/10)
Luxmanor/Hollyoak/Heritage Walk	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 for Luxmanor (BL, 8/28/08)
Manor Park	FY 00	Concrete Construction	Complete	* No concrete work in this community. (RP, 3/1/09)
Manor Park	FY 00	Drainage Improvements	Complete	* Storm drainage work at Manor Park Ct + Rd and Carrollton completed by fall of 2005. (WD, 2/6/06)
Manor Park	FY 00	Other	Complete	* Renew Montgomery work now finished. Letter from County Executive to civic leaders sent. (RP, 5/26/2009)
Manor Park	FY 00	Resurfacing	Complete	* Final micro paving completed in 2008. (RP, 1/5/09) * Resurfacing completed . (2/20/09)
Manor Park	FY 00	Tree Maintenance and/or Replanting	Complete	* Tree maintenance work. (BL, 3/1/09)
Maplewood	FY 00	Other	Complete	* See Alta Vista
Marrymont	FY 02	Other	Started	* See Stratton Woods listing.
Merrimac Park/Woodburn	FY 04	Concrete Construction	Complete	* Repairs to existing concrete curb and gutters completed by 10/04. (JB, 1/10/05) Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Merrimac Park/Woodburn	FY 04	Drainage Improvements	Unknown	* None
Merrimac Park/Woodburn	FY 04	Resurfacing	Unknown	* None
Merrimac Park/Woodburn	FY 04	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Merrimac Park/Woodburn	FY 04	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (Mrrmc Prk) + (Wdbn)(BL, 8/28/08)
Merrimac Park/Woodburn	FY 04	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Montgomery Hills/Linden	FY 03	Concrete Construction	Complete	* New sidewalk constructed on Seminary, 10/03. (RE, 12/1/2003) * Concrete work completed north of Seminary Road by spring 04. Work south of Seminary completed by 9/04. (JB, 1/10/05) * Concrete. (2/20/09)
Montgomery Hills/Linden	FY 03	Drainage Improvements	Complete	* Storm drain project on Brookville Rd and Linden La is complete. Trees have been removed from Linden and new trees are being planted along Brookville Rd. (YA & BL, 5/7/07) * Drainage system refurbishments were made on Brookeville Road under the Drainage Assistance Request Program (YA, 6/11/07)
Montgomery Hills/Linden	FY 03	Other	Complete	* Renew Montgomery work now finished. * Letter from County Executive to civic leaders sent. (RP, 5/26/2009)
Montgomery Hills/Linden	FY 03	Resurfacing	Complete	* 100% of roads now slurry sealed. Roads in the north portion (Linden) will not be done in 05's construction season. (GL, 6/6/05) * Warren St was widened due to the installation of the new curb and was re-paved in two locations, and Seminary Rd was also paved from Forest Glen Rd to Linden Lane. * Both subdivisions on the sides of Seminary Rd were Micro paved. Warren St, New Castle Av and Woodley Ave were paved because the roads were so bad we could not patch. Linden Lane will be paved after Capital Development completes a drainage project in the Spring, 08. (JH, 9/21/07) * Linden Lane is on the list for Spring. We are waiting for Capital Development's (MM's) drainage project to start and finish. (JH, 10/9/07) * Final micro paving completed in 2008. (RP, 1/5/09)
Montgomery Hills/Linden	FY 03	Resurfacing	Complete	* Total Slurry expenditure completed in 2007 (JB, 2/2/09)
Montgomery Hills/Linden	FY 03	Resurfacing	Complete	* Resurfacing completed. (2/20/09)
Montgomery Hills/Linden	FY 03	Traffic	Complete	* As a result of two traffic studies which have now been completed, the

		Engineering		<p>following recommendations were implemented:</p> <ol style="list-style-type: none"> 1. Establishment of a "School Zone" on Seminary Road/Linden Lane from Sutton Place to Monroe Street. 2. Establishment of a "School Zone" on Brookville Road from Montgomery Street to Linden Lane. 3. Installation of standard "No Parking Any Time" corner clearances at the intersection of Riley Place/Riley Road/Second Avenue. (JG, 8/19/04) <p>* Sign and Marking work completed in FY09 (JP, 1/25/10)</p>
Montgomery Hills/Linden	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Montgomery Hills/Linden	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 for Montgomery Hills (BL, 8/28/08)
North Bethesda Grove	FY 03	Concrete Construction	Complete	* Concrete work completed (DS, 6/7/04).
North Bethesda Grove	FY 03	Drainage Improvements	Complete	* Drainage system refurbishments were made on Broad Street under the Drainage Assistance Request Program (YA, 6/11/07)
North Bethesda Grove	FY 03	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
North Bethesda Grove	FY 03	Traffic Engineering	Unknown	* None
North Bethesda Grove	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
North Bethesda Grove	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
North Hills of Sligo	FY 03	Concrete Construction	Complete	* Repairs to existing concrete curb and gutters completed by 9/04. (DS, 9/13/04) Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work. (AD, 1/25/08)
North Hills of Sligo	FY 03	Drainage Improvements	Complete	* None
North Hills of Sligo	FY 03	Other	Complete	* Letter from County Executive to civic leaders sent. (ML, 3/7/2008)
North Hills of Sligo	FY 03	Resurfacing	Complete	* Final micro paving completed in fall, 2006. (GL, 3/19/08)
North Hills of Sligo	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
North Hills of Sligo	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
North Hills of Sligo	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
North Woodside	FY 00	Other	Complete	* See Rosemary Hills listing.
Northwood	FY 00	Concrete Construction	Complete	* Concrete curb and gutter work complete (2/20/09)
Northwood	FY 00	Drainage Improvements	Complete	* None
Northwood	FY 00	Other	Complete	* Renew Montgomery work now finished. Letter from County Executive to civic leaders sent. (RP, 5/26/2009)
Northwood	FY 00	Resurfacing	Complete	* Final micro paving completed in 2002. (RP, 1/5/09) * Resurfacing completed . (2/20/09)
Northwood	FY 00	Traffic Engineering	Complete	* None
Northwood	FY 00	Tree Maintenance and/or Replanting	Complete	* Trees completed. (2/20/09)
Northwood Park	FY 05	Concrete Construction	Complete	* All of the curbing work is complete in the Northwood Park Subdivision. (JB, 9/29/05) Neighborhood is completed. (AD, 11/24/08)
Northwood Park	FY 05	Drainage Improvements	Unknown	* None
Northwood Park	FY 05	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Northwood Park	FY 05	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Northwood Park	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09(per BL email 1/15/10)
Northwood Park	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance unit work (BL, 7/3/08)

Oakland Terrace	FY 07	Other	Started	* See Carroll Knolls
Oakview	FY 98	Other	Complete	* Renew Montgomery work completed.
Oranges	FY 07	Other	Started	* See Sligo Park Knolls
Parkwood	FY 05	Concrete Construction	Complete	* New ADA sidewalk work along Cedar La being constructed by DCD. (AD, 6/11/07)
Parkwood	FY 05	Concrete Construction	Complete	* Spending (AD, 1/8/07)
Parkwood	FY 05	Concrete Construction	Complete	* Concrete curb work completed (AD, 11/24/08)
Parkwood	FY 05	Drainage Improvements	Complete	* An additional drainage system refurbishment project was made in Parkwood. (AD, 1/25/08)
Parkwood	FY 05	Drainage Improvements	Complete	* Curb & gutter work is 40% completed as of June, 05. FY05 funding will not allow completion of all curb & gutter work. (JB, 8/8/05) * This work continued in the calendar 2006 construction season. Will resume in the 2007 season. (JB, 8/7/2006) * Neighborhood issues re curb and gutter work on Dresden Rd resolved with assistance of civic official Liz Brennan and work completed. Other curb work proceeding in the community. (AD, 5/7/07) * Drainage system refurbishments were made on Beech and Franklin by Highway Maintenance. (This work not under Capital Development's Drainage Assistance Request Program. (MM, 8/17/07)) An additional drainage system refurbishment project was made in Parkwood at a cost of \$30,158.58. (AD, 1/25/08)
Parkwood	FY 05	Other	Complete	* Letter from County Executive to civic leaders sent. (ML, 7/1/2008)
Parkwood	FY 05	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling the amount shown in the cost field. (JP, 1/25/10) * Regarding the traffic study at the intersection of Saul Road and Wildwood Road and the intersection of Saul Road and Woodfield Road, in which community requested multi-way stop controls at these intersections: Traffic Engineering & Operations (TEOS) has initiated a traffic study at these intersections last year. The traffic data has been collected and will be analyzed for the final conclusions. TEOS will advise you our recommendations soon when the study is approved. (Kyle Liang, Senior Planning Specialist, 4/11/07)
Parkwood	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Parkwood	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance (BL, 6/16/08)
Plyers Mill Estates	FY 07	Other	Started	* See Carroll Knolls
Randolph Farms/Randolph Hills	FY 01	Concrete Construction	Complete	* None
Randolph Farms/Randolph Hills	FY 01	Drainage Improvements	Complete	* None
Randolph Farms/Randolph Hills	FY 01	Other	Complete	* Renew Montgomery work now finished. * Letter from County Executive to civic leaders sent. (TP, 5/2006)
Randolph Farms/Randolph Hills	FY 01	Resurfacing	Complete	* Final surface repairs, preparation, and resurfacing of roads completed. (GL, 12/12/05)
Randolph Farms/Randolph Hills	FY 01	Traffic Engineering	Complete	* None
Regency Estates	FY 99	Other	Complete	* Renew Montgomery work completed.
Rock Creek Hills	FY 03	Concrete Construction	Complete	* Completed sidewalk and curb work was completed (AD, 4/22/08) * Concrete work completed by mid May, 04. (DS, 6/7/04)
Rock Creek Hills	FY 03	Drainage Improvements	Complete	* None
Rock Creek Hills	FY 03	Other	Complete	* Letter from County Executive to civic leaders sent. (ML, 7/1/2008)
Rock Creek Hills	FY 03	Resurfacing	Complete	* Final micro paving completed in spring, 2007. (GL, 11/5/07) * Resurfacing completed 06/07 (JB, 2/2/09)
Rock Creek Hills	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Rock Creek Hills	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10) * Tree Maintenance unit work (7/18/08,BL)
Rock Creek Palisades	FY 99	Other	Complete	* Letter from County Executive to civic leaders sent. (TP, 1/04)

Rollingwood	FY 03	Concrete Construction	Complete	* Total concrete work investment (AD, 1/25/08)
Rollingwood	FY 03	Drainage Improvements	Complete	* Curb and gutter work complete. * Two drainage projects—Leland (by Div of Cap Devel) & Woodbine (by Hwy Main) have been done by same contractor in FY06. (JB, 12/12/05)
Rollingwood	FY 03	Other	Complete	* Letter from County Executive to civic leaders sent. (ML, 3/7/2008)
Rollingwood	FY 03	Resurfacing	Complete	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work. * Final micro paving completed in spring, 2007. (GL, 3/19/08)
Rollingwood	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Rollingwood	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Rollingwood	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
Rosemary Hills/North Woodside	FY 00	Concrete Construction	Complete	* None
Rosemary Hills/North Woodside	FY 00	Drainage Improvements	Complete	* Concrete curb and gutter work complete. (AD, 11/24/08)
Rosemary Hills/North Woodside	FY 00	Other	Complete	* Renew Montgomery work now finished. CE letter mailed. (TP, 5/2006)
Rosemary Hills/North Woodside	FY 00	Resurfacing	Complete	* All final surface repairs, preparation, and resurfacing of roads completed in FY04. (GL, 12/12/05)
Rosemary Hills/North Woodside	FY 00	Traffic Engineering	Complete	* None
Sligo Park Knolls/Oranges/Breewood Manor	FY 07	Concrete Construction	Complete	* Concrete work underway. (AD, 11/5/07) * Concrete work is 10% completed. (7/7/08, JB) * Concrete work completed only on Tenbrook Rd from Dennis to the dead end. Tenbrook has been milled and overlaid. (JB, 10/6/08) * Concrete work completed for the season. (AD, 11/24/08) * Curb & gutter work projected to continue this construction season, 09. (JB, 7/16/09) * Scheduled to continue concrete repairs this fall. (RPaugh 12/1/10) * Concrete work 10% complete. (DHS construction report, 6/11/11) * Newsletter sent to community. (5/31/11) * Concrete work 50% complete. (DHS construction report, 10/14/11) Concrete work 85% complete. (DHS construction report 11/11/11). * Concrete work now complete. (DHS construction report, 10/13/12)
Sligo Park Knolls/Oranges/Breewood Manor	FY 07	Drainage Improvements	Unknown	* None
Sligo Park Knolls/Oranges/Breewood Manor	FY 07	Other	Complete	* Community Outreach Office sends to civic organization contact and introductory letter announcing neighborhood selection for Renew Montgomery program. (3/2/07)
Sligo Park Knolls/Oranges/Breewood Manor	FY 07	Resurfacing	Complete	* We completed repaving Tenbrook Rd. this summer/fall. (RP, 1/5/09) * Concrete repairs in this area are scheduled to start around the middle of September and should take approx. 2 months to complete. (JB 8/5/10) * Permanent patching complete 10/5/2012 - (DHS by- weekly stat report 11/24/2012)
Sligo Park Knolls/Oranges/Breewood Manor	FY 07	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Sligo Park Knolls/Oranges/Breewood Manor	FY 07	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 for Sligo Park Knolls (BL, 8/28/08)
Sligo Park Knolls/Oranges/Breewood Manor	FY 07	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
South Four Corners	FY 06	Concrete Construction	Complete	* We will be installing concrete curb and gutter on virtually every road within our boundaries in South Four Corners. We want to stick to our boundaries for Renew Montgomery work because our Residential Concrete Repair Program passed through the rest of the area (from Renfrew to Tenbrook) back in 1998 – 1999. (JB, 7/13/06) * All concrete work done for this season. (AD, 10/1/07) * Concrete work is 75% completed. (7/7/08, JB) * All concrete work is completed (AD, 7/17/2009)
South Four Corners	FY 06	Concrete Construction	Complete	* Additional investment (AD 7/17/09)
South Four Corners	FY 06	Drainage Improvements	Started	* We are currently studying Hereford Place and Perth Place for inclusion in the curbing process and I am 90% certain that they will be included.

				The roads are wide enough and we really don't have any obstructions except for Hereford Pl. just above Perth where a large tree is located. That section will not receive curbing because we cannot take down trees during this process. We have plenty of drainage structures to carry the water to, so drainage is not a problem. (JB, 5/3/06)
South Four Corners	FY 06	Resurfacing	Complete	*Permanent patching work completed,by 8/30/2012. (DHS By-Weekly Status Report 11/24/2012)
South Four Corners	FY 06	Traffic Engineering	Complete	* Existing streetlights were upgraded and new streetlights were installed in FY98. (MC, 4/10/06) * Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Stratton Woods/Marrymont	FY 02	Concrete Construction	Complete	* Concrete work completed by 7/04 (DS, (1/1/04).
Stratton Woods/Marrymont	FY 02	Drainage Improvements	Unknown	* None
Stratton Woods/Marrymont	FY 02	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Stratton Woods/Marrymont	FY 02	Traffic Engineering	Unknown	* None
Sumner	FY 05	Concrete Construction	Complete	* Concrete curb & gutter work was completed during the summer 05 construction season. (JB, 10/3/05) Completed (AD, 11/24/08)
Sumner	FY 05	Drainage Improvements	Complete	* Highway Maintenance is constructing a new storm drain system along Bolton Rd from Overlea Rd to Ft. Sumner to serve the Ft. Sumner to Falls Branch basin. This project is projected to be completed in the fall, 2007. (YA, 5/7/07)
Sumner	FY 05	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Sumner	FY 05	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Sumner	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance unit work done for FY09 (per BL email 1/15/10)
Sumner	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
Tamarack Triangle	FY 97	Other	Complete	* Renew Montgomery work completed.
Veirs Mill Village	FY 97	Other	Complete	* Renew Montgomery work completed.
Walnut Hills	FY 03	Concrete Construction	Complete	* Repairs to existing concrete curb and gutters were completed in September, 04. (DS, 9/22/04)
Walnut Hills	FY 03	Drainage Improvements	Complete	* Drainage system refurbishments were made on Chestnut Street under the Drainage Assistance Request Program (YA, 6/11/07)
Walnut Hills	FY 03	Other	Started	Renew Montgomery work now finished. Close out letter TP office for review RP 3/15/11
Walnut Hills	FY 03	Resurfacing	Complete	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work. * Final road repairs and micro sealing will not occur until probably in FY09. (R. Dorsey, 10/17/06) * Highway Maintenance has scheduled this neighborhood for hot mix asphalt resurfacing work on its FY10 schedule. (JB, 7/16/09) * Resurfacing was completed in May 2010 (JB 8/5/10)
Walnut Hills	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Walnut Hills	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Walnut Hills	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
West Bethesda Park	FY 03	Other	Started	* See Woodhaven/Highland Hills listing.
Westchester	FY 00	Concrete Construction	Complete	* Concrete completed . (2/20/09) * Concrete curb and gutter work complete.
Westchester	FY 00	Drainage Improvements	Complete	* None
Westchester	FY 00	Other	Complete	* Renew Montgomery work now finished. Letter from County Executive to civic leaders sent. (RP, 5/26/2009)
Westchester	FY 00	Resurfacing	Complete	* Final micro paving completed in 2003. (RP, 1/5/09) * Resurfacing completed . (2/20/09)
Westchester	FY 00	Traffic	Complete	* None

		Engineering		
Westchester	FY 00	Tree Maintenance and/or Replanting	Complete	*Tree maintenance work. (BL, 3/1/09)
Westgate/Crestview/Westhaven	FY 02	Concrete Construction	Complete	* All concrete work completed as of 4/4/05. (JB, 6/6/05) * All existing concrete curbs except for two remaining roads refurbished as of 8/2/04. (DS, 8/2/04)
Westgate/Crestview/Westhaven	FY 02	Drainage Improvements	Unknown	* None
Westgate/Crestview/Westhaven	FY 02	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Westgate/Crestview/Westhaven	FY 02	Traffic Engineering	Unknown	* None
Westhaven	FY 02	Other	Started	* See Westgate listing.
Westmorland Hills	FY 07	Concrete Construction	Complete	* Concrete work 45% completed, including new curb and gutter on Jamestown Rd. (AD, 7/16/07) * We are now 85% completed and will return in FY09. (AD, 1/7/08) * Concrete work is completed (AD, 11/24/08)
Westmorland Hills	FY 07	Concrete Construction	Complete	* Additional investment(AD 7/17/09)
Westmorland Hills	FY 07	Drainage Improvements	Complete	* Drainage system refurbishments were made on Jamestown at Albemarle under the Drainage Assistance Request Program (YA, 6/11/07)
Westmorland Hills	FY 07	Other	Complete	* Community Outreach Office sends to civic organization contact and introductory letter announcing neighborhood selection for Renew Montgomery program. (3/7/07)
Westmorland Hills	FY 07	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Westmorland Hills	FY 07	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Westmorland Hills	FY 07	Tree Maintenance and/or Replanting	Complete	* Highway Maintenance has removed three dead trees in FY07 thus far. (BL, 1/29/07) * Tree Maintenance work from FY04 to FY08 (BL, 8/28/08)
Westmorland Hills	FY 07	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance unit work done for FY09 (per BL email 1/15/10)
Wheaton Woods	FY 09	Concrete Construction	Complete	* 6/29/10 HWY Services sends newsletter to residents advising of concrete repairs coming soon to their neighborhood (RP, 7/12/10) * Highway Services sends second newsletter to residents in an another part of this designated Renew Montgomery community advising of concrete repairs coming soon to their neighborhood." (RP, 7/22/10) * Concrete work 100% complete. (DHS construction report, 10/14/11)
Wheaton Woods	FY 09	Drainage Improvements	Started	* DEP doing some storm drain inlets, retrofitting. * DEP undertaking a Greestree pilot--adding in rainscape and natural treatments in the right of way along with storm drainage treatments. DEP is looking at Grenoble and several other local streets. DEP is also meeting with homeowners to discuss rain gardens, rain barrels, etc. to install on private property. 30 percent resident participation would trigger contractor-installed raingardens at County expense. (P.Rowe, 8/3/09)
Wheaton Woods	FY 09	Other	Complete	* Community Outreach Office sent to civic organization contacts introductory letter announcing neighborhood selection for Renew Montgomery program. (3/10/09) * CONFIRM THIS NEIGHBORHOOD READY FOR CLOSE OUT. (11/7/11) * Resurfacing work 100% complete. (DHS construction report, 10/14/11) – but per RP, the W side of Parkland Dr is done, but E side still needed. (12/5) THIS NEIGHBORHOOD IS NOT YET READY FOR CLOSE OUT. (12/5/11)
Wheaton Woods	FY 09	Resurfacing	Complete	* Resurfacing work 100% complete within FY12 summer-fall construction season. (DHS construction report, 10/14/11) – but per JB, this only refers to area EAST of Parkland Dr. (11/7/11) Rersurfacing work 100% complete - but per JB, this only refers to area EAST of Parkland DR.. (DHS construction report 10/14/11) * Highway Services sends newsletter to residents advising of resurfacing to begin in their neighborhood on or about June 6, 2011. (TP, 2/6/12)
Wheaton Woods	FY 09	Traffic Engineering	Complete	* Sign and Marking work done in FY09(JP, 1/25/10) * Streetlight unit installed in FY09 2 – 70 W, HPS Streetlights at 4705 Falcon Street (TS, 1/4/10)

				* Streetlight unit trimmed trees for lighting in FY09 at Justice Road between Aspen Hill Road and Grenoble Drive and at 14008 Parkland Drive. (TS, 1/4/10)
Wheaton Woods	FY 09	Tree Maintenance and/or Replanting	Complete	* As crews start concrete work they elevate trees. (RP, 10/5/10) * Tree work expenditures in FY09 (BL, 11/10/09)
Wohlshire	FY 06	Concrete Construction	Complete	* Concrete work is 20% completed. (7/7/08, JB) Work is scheduled for summer of 08. (AD, 6/2/08) * Concrete work stopped for the season, will start back up in the summer, 09. (AD, 11/24/08) * Curb & gutter work 50% complete. (RP, 1/5/09) * Remaining concrete work was surveyed by contractor. Additional curb and gutter work deemed not appropriate due to drainage concerns. Apron work now being offered at a discount to residents. No other concrete work will be scheduled for this neighborhood under Renew Montgomery. (JB, 7/6/09) *Concrete Completed (AD 7/17/09)
Wohlshire	FY 06	Drainage Improvements	Unknown	* None
Wohlshire	FY 06	Other	Complete	Note: Most of Wohlshire is in the Brookdale civic association. (per Larry Howe, 7/25/2006)
Wohlshire	FY 06	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Wohlshire	FY 06	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Woodacres	FY 99	Other	Complete	* Renew Montgomery work completed.
Woodburn	FY 04	Other	Started	* See Merrimac Park listing
Woodburn	FY 04	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10) * Brett has 2 separate totals for Merrimac Park and Woodburn. The total below is for Woodburn.
Woodhaven/Highland Hills (also known as Bradley Park/West Bethesda Park)	FY 03	Concrete Construction	Complete	* Concrete work completed by 7/03. (DS, 11/3/03)
Woodhaven/Highland Hills (also known as Bradley Park/West Bethesda Park)	FY 03	Drainage Improvements	Unknown	* None
Woodhaven/Highland Hills (also known as Bradley Park/West Bethesda Park)	FY 03	Other	Started	* Letter sent to CE for signature. (TP, 12/22/09)
Woodhaven/Highland Hills (also known as Bradley Park/West Bethesda Park)	FY 03	Resurfacing	Complete	* Resurfacing is complete in 2007 (JB, 2/2/09)
Woodhaven/Highland Hills (also known as Bradley Park/West Bethesda Park)	FY 03	Traffic Engineering	Unknown	* None
Woodmoor/Indian Spring Village	FY 03	Concrete Construction	Complete	* Repairs to existing concrete curb and gutters completed 5/07 (JB) * "I am writing to express our gratitude to you and your crew for the outstanding job they did in putting in curbs, sidewalks and aprons on Eastmoor Drive!! A special commendation should go to Dan Edwards, because without him, I fear the project would have never been completed! Dan did an OUTSTANDING job dealing with the many obstacles he encountered on the street. Needless to say, we are all so pleased with the beautification of our street. It looks wonderful! Sincerely, Maria Warner" (9/10/07) * This project was very controversial last year. The residents were polarized over the loss of 25-mature trees. It was determined several years ago that the trees must be removed in order to install new curb and gutters. This issue of tree removal reached the State Arborist as well as the County Executive and also involved a Delegate. Some residents wanted to save the trees, some wanted the new curbs. The Division of Highway Services was able to give them both! (KC, 9/12/07)
Woodmoor/Indian Spring Village	FY 03	Drainage Improvements	Unknown	* None
Woodmoor/Indian Spring Village	FY 03	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.

Woodmoor/Indian Spring Village	FY 03	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Woodmoor/Indian Spring Village	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Woodmoor/Indian Spring Village	FY 03	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance unit work FY 04-08 (BL, 6/9/08)
Woodside Forest	FY 00	Other	Complete	* Letter from County Executive to civic leaders sent. (TP, 1/04)
Woodside Park	FY 97	Other	Complete	* Completed in 1999. (JB, 2/15/05)
Woodside Park East	FY 04	Concrete Construction	Complete	* Concrete curb and gutter work has been completed as June, 05. (JB, 6/9/05) * Concrete curb and gutter work total expenditure (RP, 12/10/09) * New sidewalk installed on Dale Dr at Dartmouth Av in FY11 by Division of Transportation Engineering (RE, 2/9/12 spreadsheet)
Woodside Park East	FY 04	Drainage Improvements	Complete	* Drainage system refurbishments were made on Greenbrier Drive under the Drainage Assistance Request Program (YA, 6/11/07)
Woodside Park East	FY 04	Other	Complete	* Letters sent to CE for signature. (TP, 12/22/09)
Woodside Park East	FY 04	Resurfacing	Complete	* Micro paving east of Dale and north of Wayne completed Sep. 07. (GL, 10/1/07) * Mainline overlay being done on Wayne and coming through this Renew Mont neighborhood. (JB, 10/1/07) * Hot mix asphalt being applied in this neighborhood in October, 08. (JB, 10/6/08)
Woodside Park East	FY 04	Traffic Engineering	Complete	* Sign and Marking work done in FY09 (JP, 1/25/10)
Wyngate/Ashburton/Alta Vista Terrace	FY 05	Concrete Construction	Complete	* Additional investment (AD 7/17/09)
Wyngate/Ashburton/Alta Vista Terrace	FY 05	Concrete Construction	Complete	* The 2007 season will focus on installing NEW curbs where none currently exist. Affected neighborhoods must achieve consensus on wanting or not wanting new curbs by this point. (JB, 8/7/2006) * Highway Maintenance should complete this area by the end of 07 construction season--sidewalk and curb work is about 80% done. (AD, 12/4/06). * Two streets have been added (Wyngate Dr. and Singleton Rd.) and we will be installing new concrete curbs; also Oakmont Pl. will get the full treatment. (sidewalk, curb, and paving) in FY09. (AD, 1/7/08) * Final completion pending Kentstone. Highway Services intends to petition the residents on this street in the fall, 09. If support shown, would propose installing new gutters under the FY10 program. (RP, 1/5/09) * Concrete work completed in fall, 07, including new gutter installed on Singleton & Wyngate. (AD, 11/5/07) Completed total investment is shown in the cost field. (AD, 11/24/08)
Wyngate/Ashburton/Alta Vista Terrace	FY 05	Drainage Improvements	Complete	* Drainage system refurbishments were made on Beech Avenue under the Drainage Assistance Request.
Wyngate/Ashburton/Alta Vista Terrace	FY 05	Resurfacing	Not Started	* Ready for final surface repairs, preparation, and resurfacing of roads to complete Renew Montgomery work.
Wyngate/Ashburton/Alta Vista Terrace	FY 05	Traffic Engineering	Complete	* Sign and Marking work done in FY09 totaling (JP, 1/25/10)
Wyngate/Ashburton/Alta Vista Terrace	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance work done for FY09 (per BL email 1/15/10)
Wyngate/Ashburton/Alta Vista Terrace	FY 05	Tree Maintenance and/or Replanting	Complete	* Tree Maintenance unit work (BL, 5/23/08)

TABLE 2
RENEW MONTGOMERY EXPENDITURES BY FISCAL YEAR AND TYPE OF WORK
 FY 97-12
 Effective: May 20, 2013

BUDGET ITEM	FISCAL YEAR				TOTAL
Capital Improvemt Prog (CIP)	<u>1997-2009</u>	<u>2010</u>	<u>2011</u>	<u>2012</u>	<u>TOTAL</u>
Sidewalks, Curb & Gutter-refb	\$35,367,961	\$6,150,307	\$2,257,587	\$1,621,124	\$45,396,979
Sidewalks, New	\$2,586,842	\$21,129	\$6,891	\$68,151	\$2,683,013
ADA Improvements	\$996,820				\$996,820
Slurry*	\$20,990	\$0			\$20,990
Traffic Calming	\$250,230				\$250,230
Streetlights	\$223,949	\$10,619		\$63,000	\$297,568
Bus Stop Amenities*(Shelters)**	\$44,030	*,**	*,**	*,**	\$44,030
Bus StopPads**	\$6,240	*,**	*,**	*,**	\$6,240
Storm Drains, New	\$1,043,577	\$0		\$68,151	\$1,111,728
Storm Drains, Repair	\$278,110	^^	^^	^^	\$278,110
Storm Water Mgtmnt, DEP^^^					
Roadway Reforestation***	\$2,500	***	***	***	\$2,500
CIP Total	\$40,821,249	\$6,182,055	\$2,264,478	\$1,820,426	\$51,088,208
Operating Budget	<u>1997-2009</u>	<u>2010</u>	<u>2011</u>	<u>2012</u>	<u>TOTAL</u>
Roadway, Base Repairs & Resurface	\$5,258,017	\$561,926	\$473,420	\$175,000	\$6,468,363
Slurry*	\$4,665,648	\$0			\$4,665,648
Signs & Markings	\$712,541	\$43,308	\$63,337	\$88,680	\$907,866
Bus Stop Amenities*,**	\$8,220	^	^	^	\$8,220
Tree Maintenance	\$4,601,361				\$4,601,361
Neighborhood Beautification	\$750	\$0	\$0	\$0	\$750
Operating Budget Total	\$15,246,537	\$605,234	\$536,757	\$263,680	\$16,652,208
TOTAL	\$56,067,786	\$6,787,289	\$2,801,235	\$2,084,106	\$67,740,416

- * Slurry & Bus stop amenities moved fr CIP to Op bud – FY98. FY09 CIP began funding some slurry work.
- ** Bus stop and ADA ramp investments are now included in Sidewalk – refurbished or new – categories.
- *** The Roadway Reforestation Grant program completed its available funding in FY00.
- ^ Bus stop pads and sidewalk connectors included in CIP sidewalk, curb, gutter refurbishment program.
- ^^ Storm drain repairs included in concrete work (sidewalk, curb and gutter refurbishment)
- ^^^ Low impact development facilities installed by Department of Environmental Protection.

SAMPLE LETTER

FROM CIVIC ASSOCIATION OFFICIAL IDENTIFYING NEIGHBORHOOD ISSUES

TO: Tom Pogue, Community Outreach Manager
Montgomery County Department of Transportation
101 Monroe Street, 10th floor
Rockville, MD 20850-2540

or

tom.pogue@montgomerycountymd.gov

We would like to submit the following list of projects for consideration in the Renew Montgomery program.

*Linden Lane — Upgrade the sidewalk basically from the intersection of Brookville to the Linden Bridge. We have received more written and oral comments about the lack of real sidewalks on this road. The existing “sidewalk” is made of asphalt. The curbing and drainage also infrastructure needs to be repaired.

Storm drains along this stretch - rain water pools in the street.

*Storm drain repair — Linden and Monroe

*Gutters/curbing — Monroe Street

One homeowner writes that their address is xxxx Seminary but our driveway access is on Monroe. When it rains, a lot of the water that rushes down Monroe on our side of the street ends up at the bottom of our driveway.

*New Street Light - Seminary Place adjacent to the Montgomery Hills Park. This poorly lit area sits at the entrance to the park. Also serves as the crossing point across Seminary Road. This is a traffic and pedestrian safety issue.

*Crosswalks - Seminary Road at Brookville Rd and Park

Repaint existing crosswalk

Line at stop sign on Seminary Place

*Road — Second Ave/Landsdown

Asphalt Road repair

*Gutter/curbs — Riley Place, Riley Road

Replace.

*Bus stops — Seminary Road


Bus stop and or benches

Any questions, please contact me at xyz@email.com or 301-123-4567.

Sincerely,

XXXXXX

President, ABC Civic Association



Maps of


FY02

**RENEW MONTGOMERY
NEIGHBORHOODS**

*Maps produced by
Joseph Pospisil*

*Division of Traffic Engineering and Operations
Department of Transportation*

Hillandale Heights

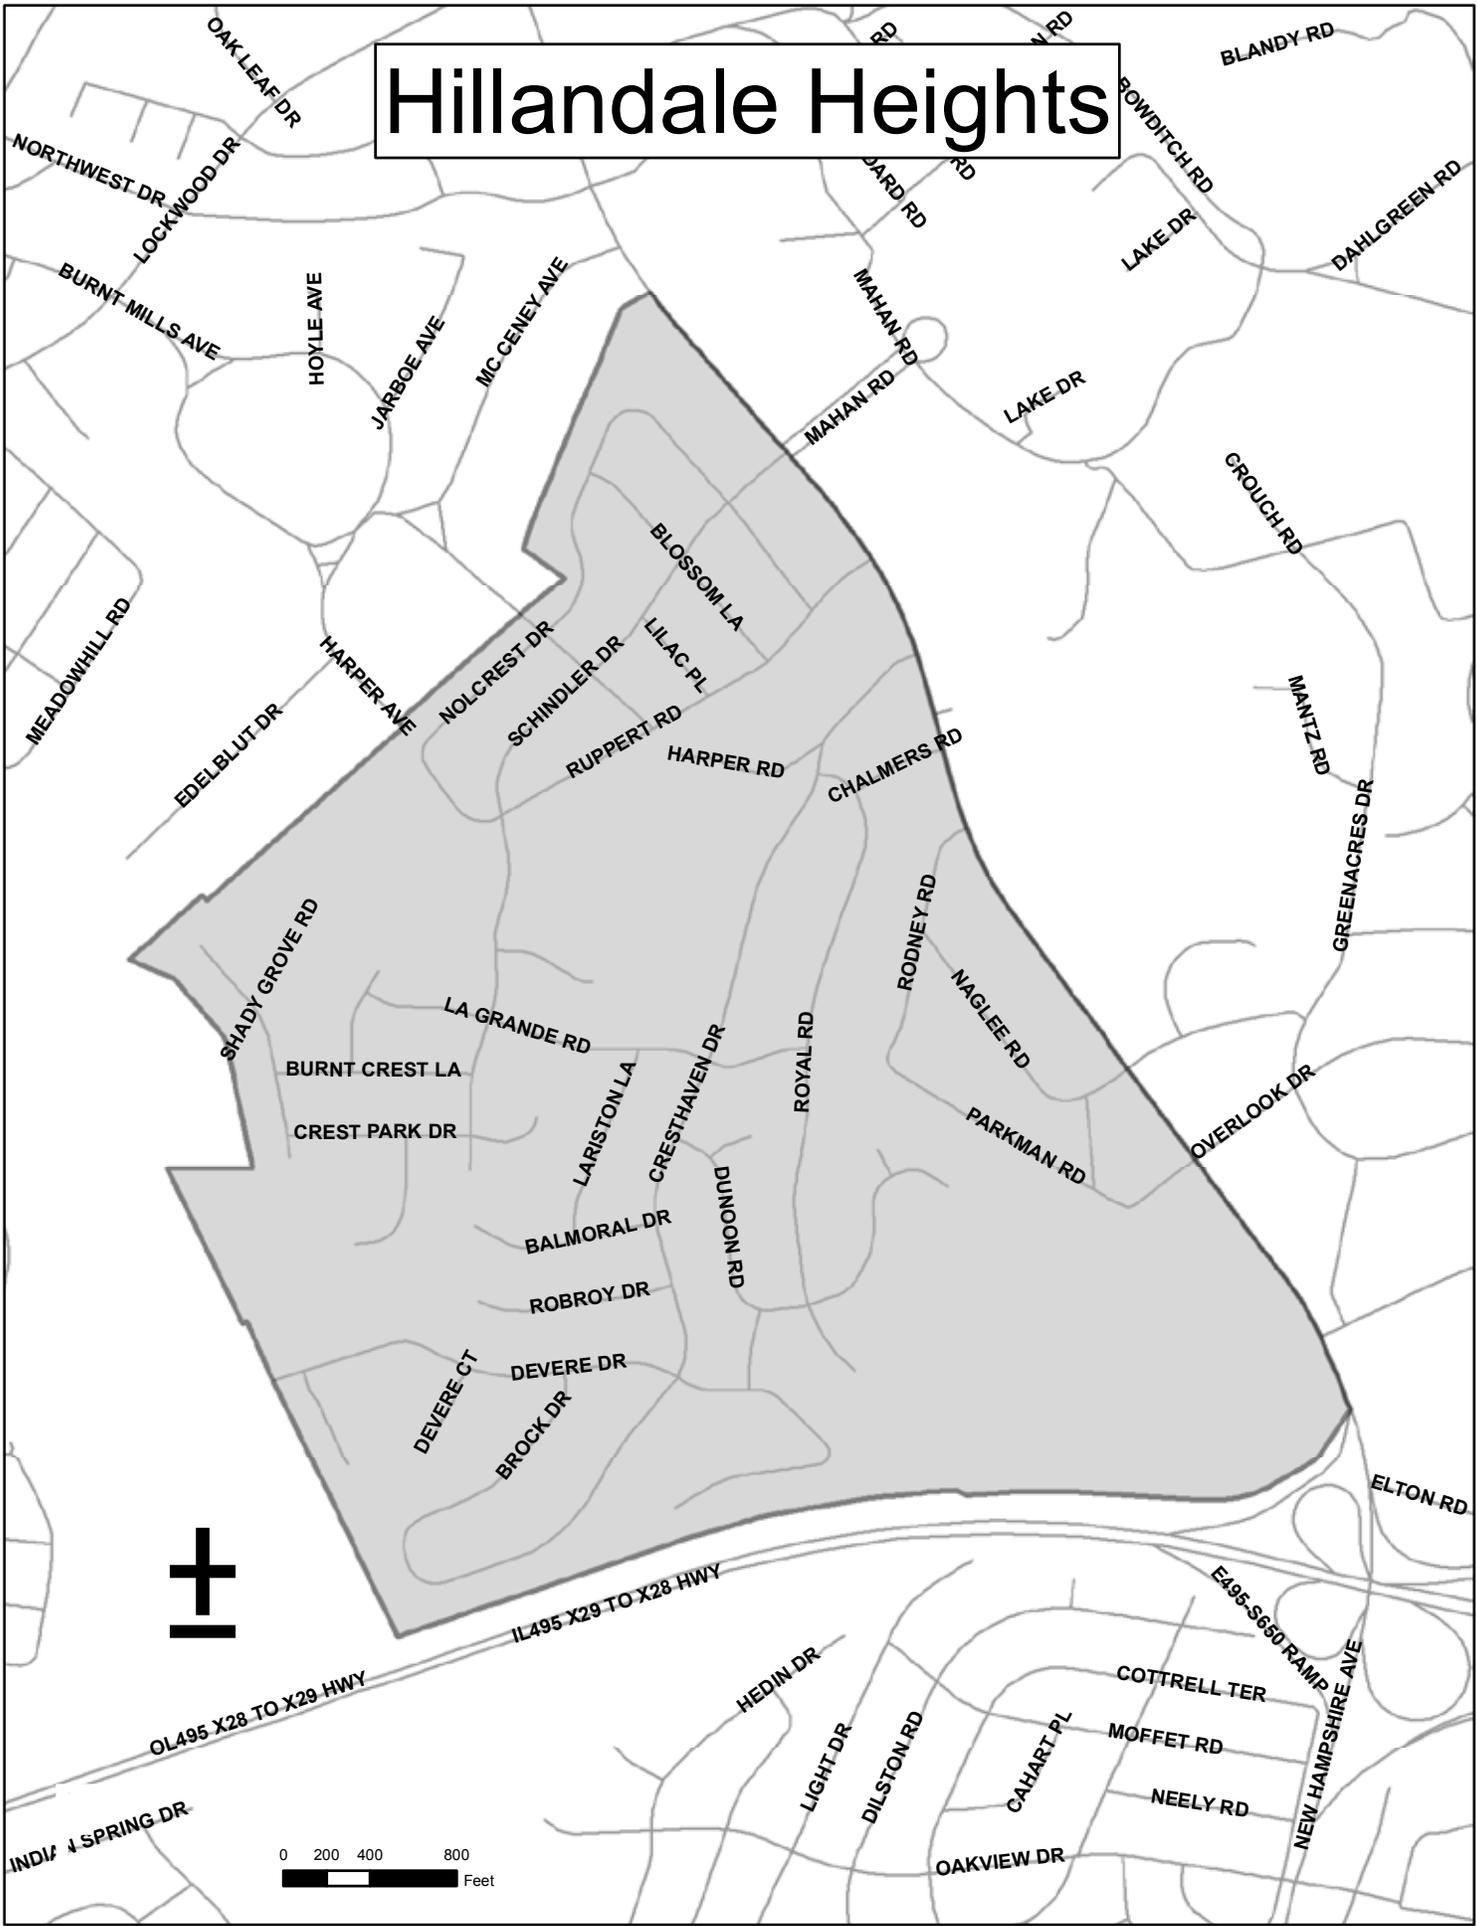


Stratton Woods/Marymount



Westgate/Crestview/Westhaven





Maps of


FY03

**RENEW MONTGOMERY
NEIGHBORHOODS**


*Maps produced by
Joseph Pospisil*

*Division of Traffic Engineering and Operations
Department of Transportation*


Calverton

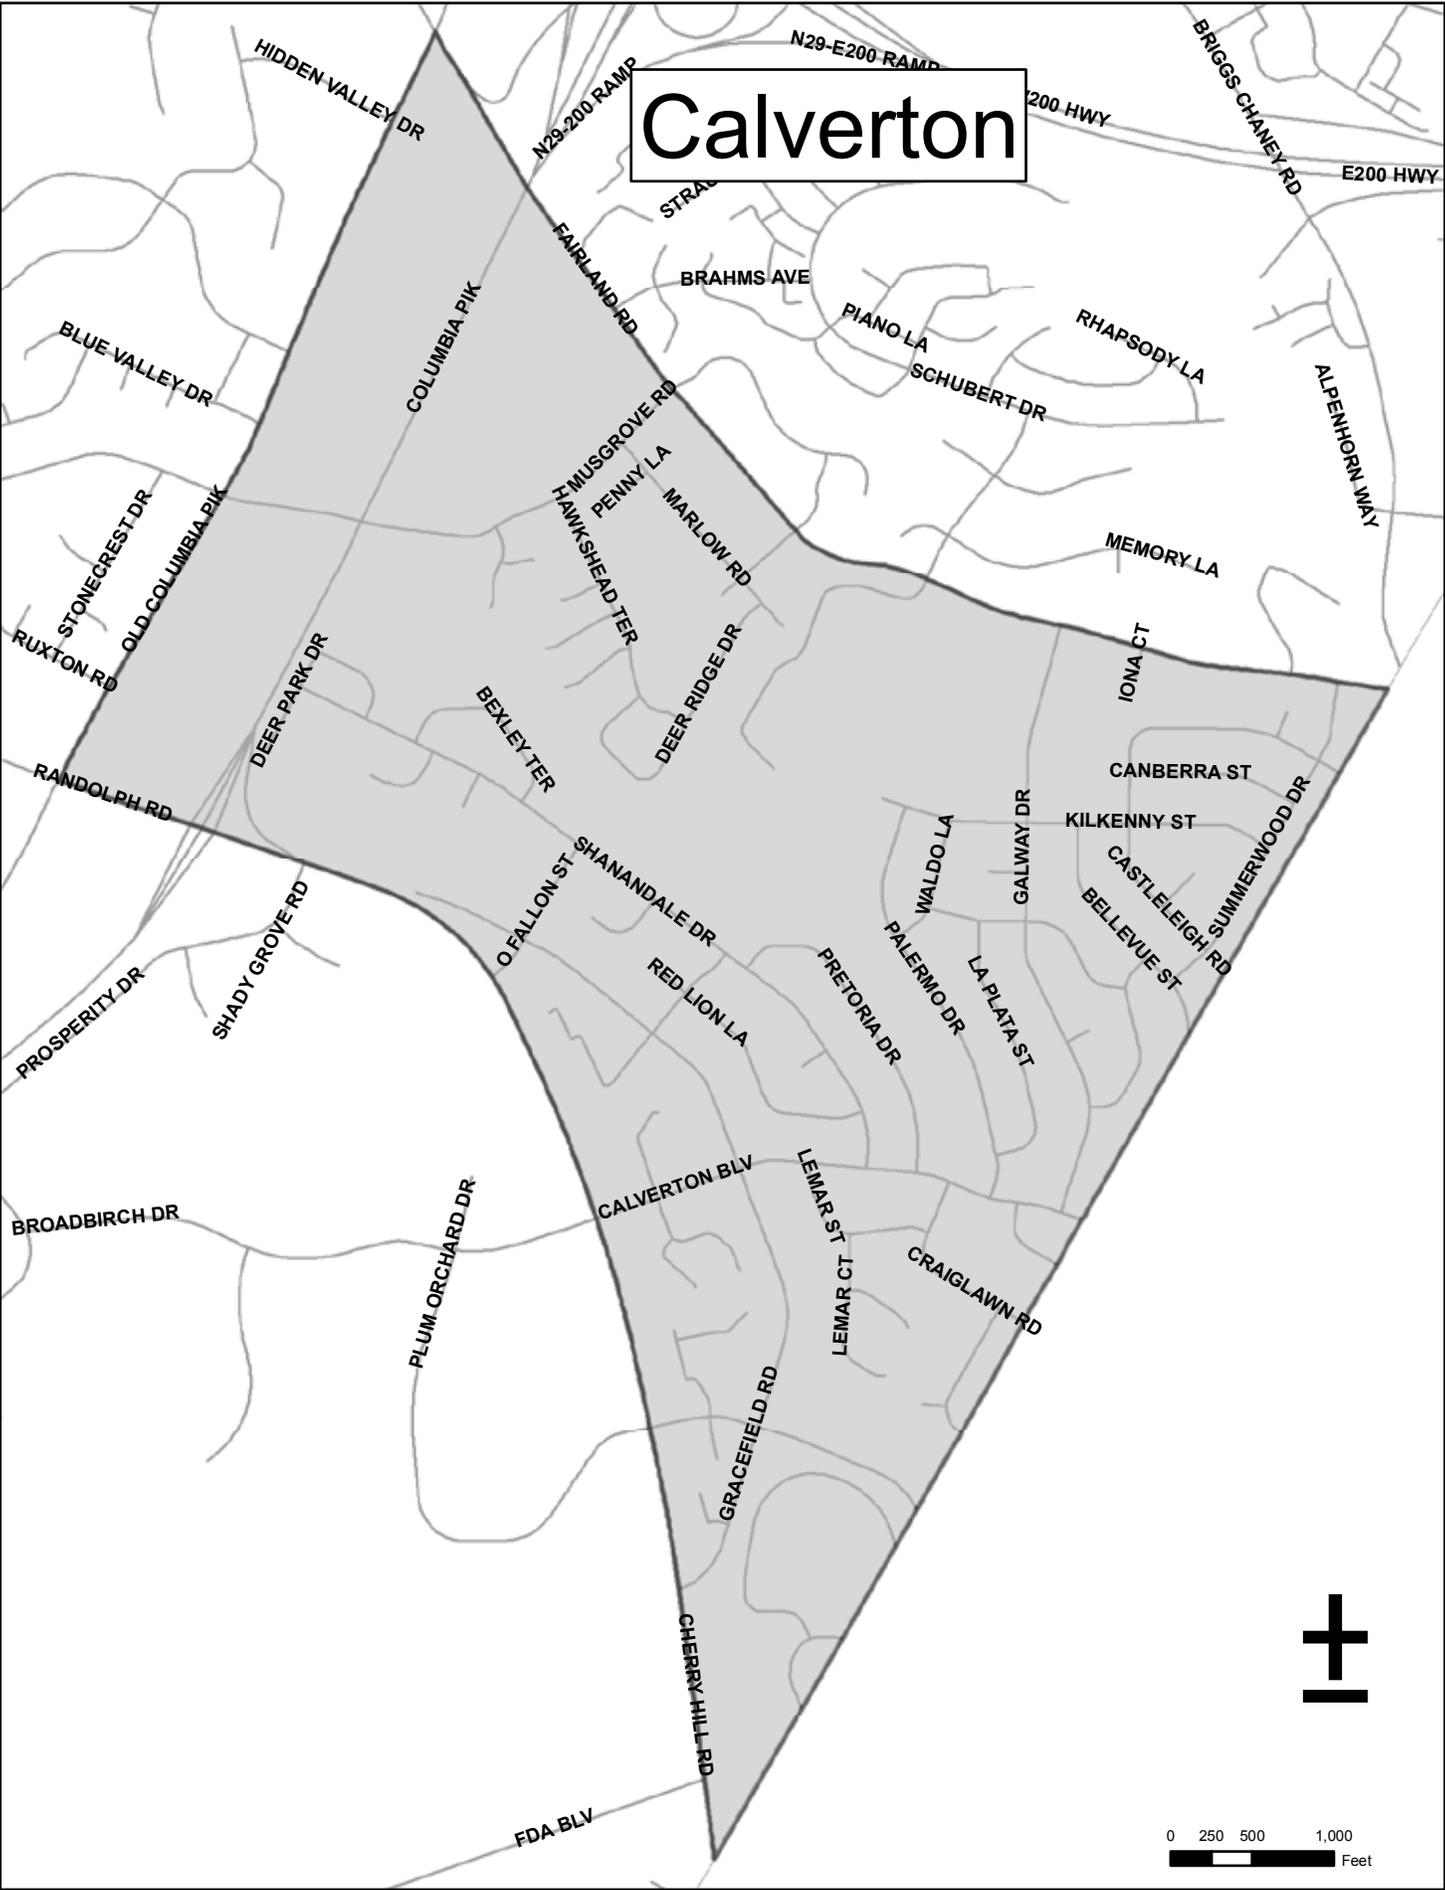

Hillandale - East of New Hampshire Ave

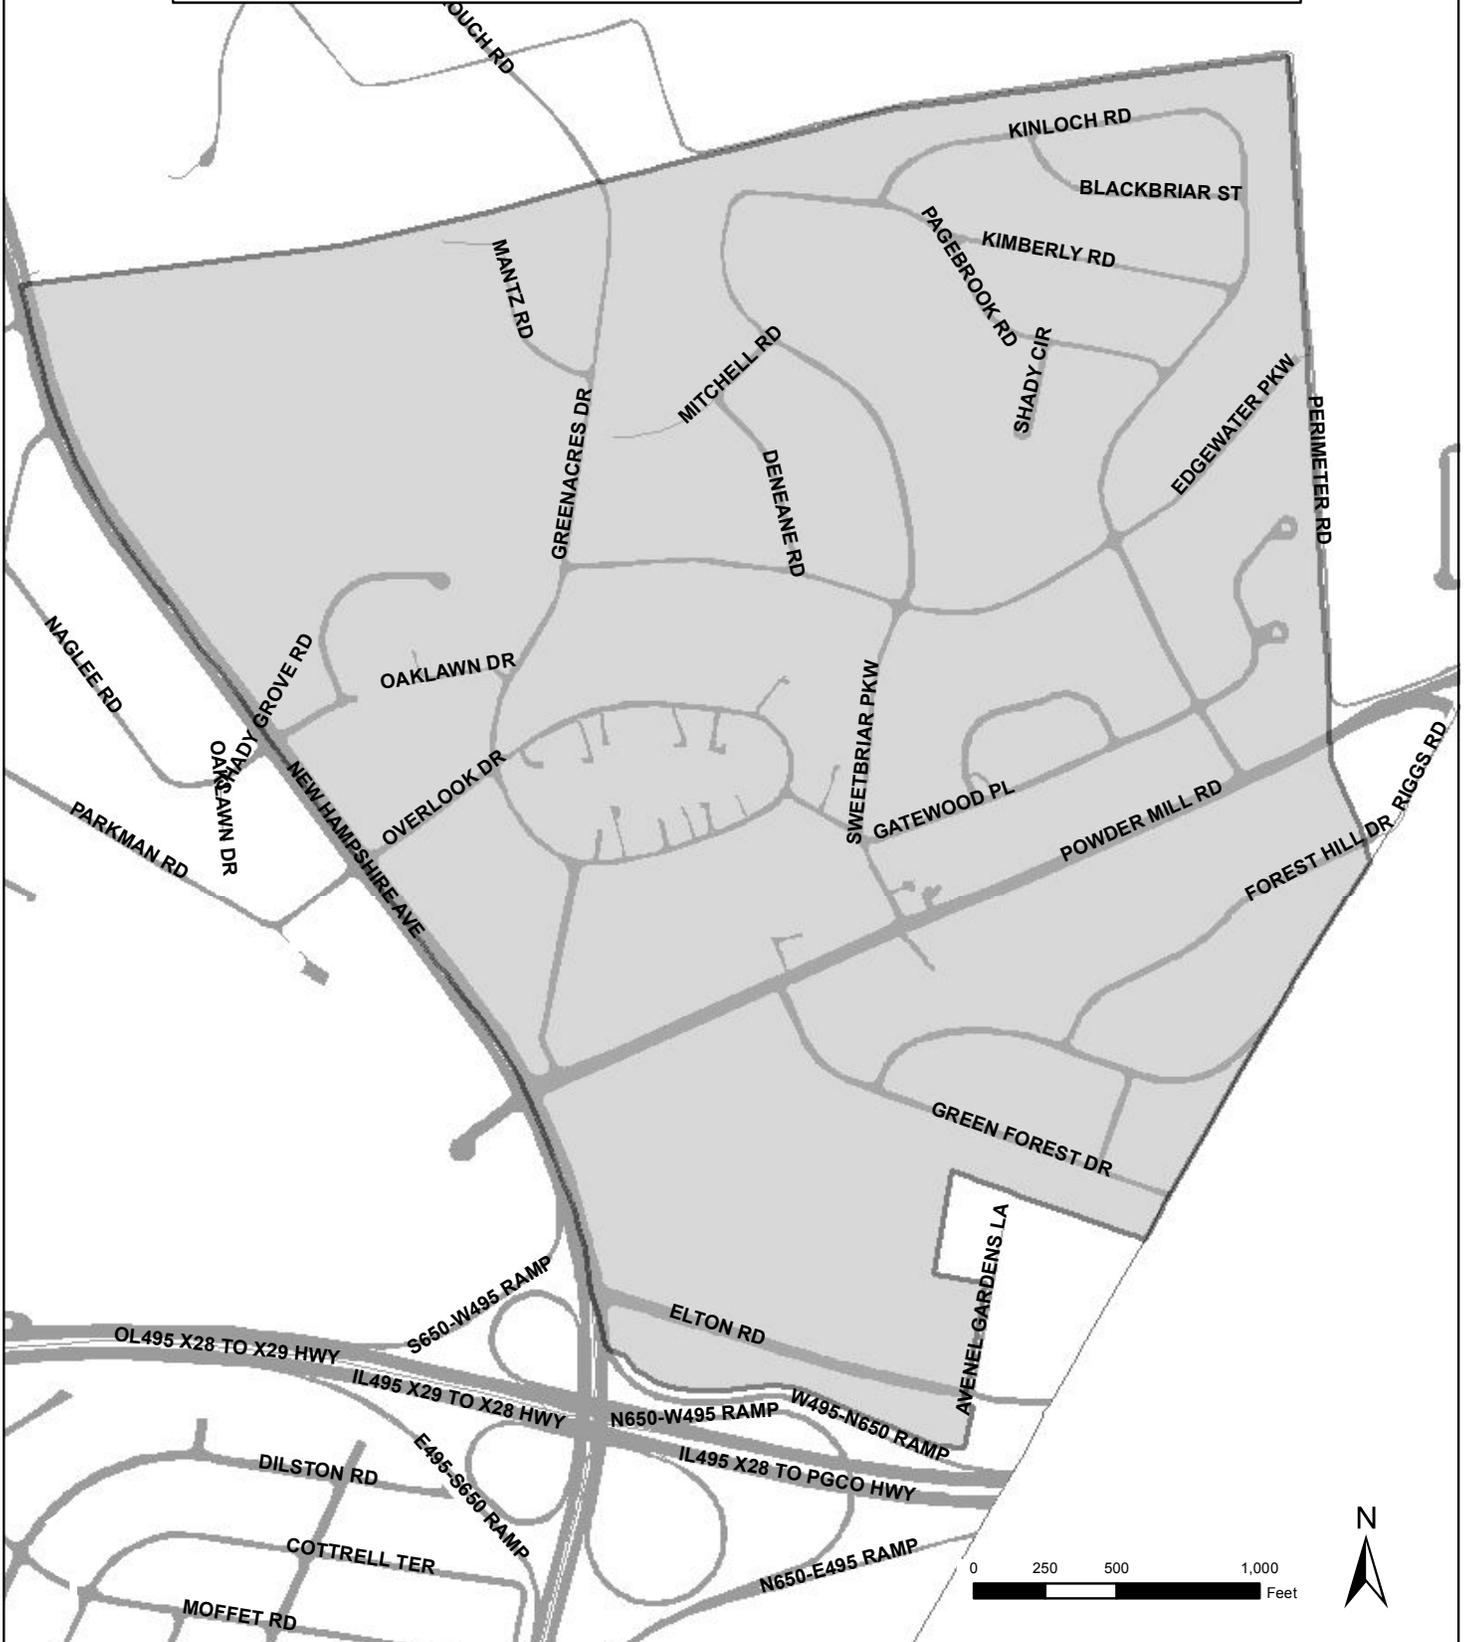


Homewood/Capital View

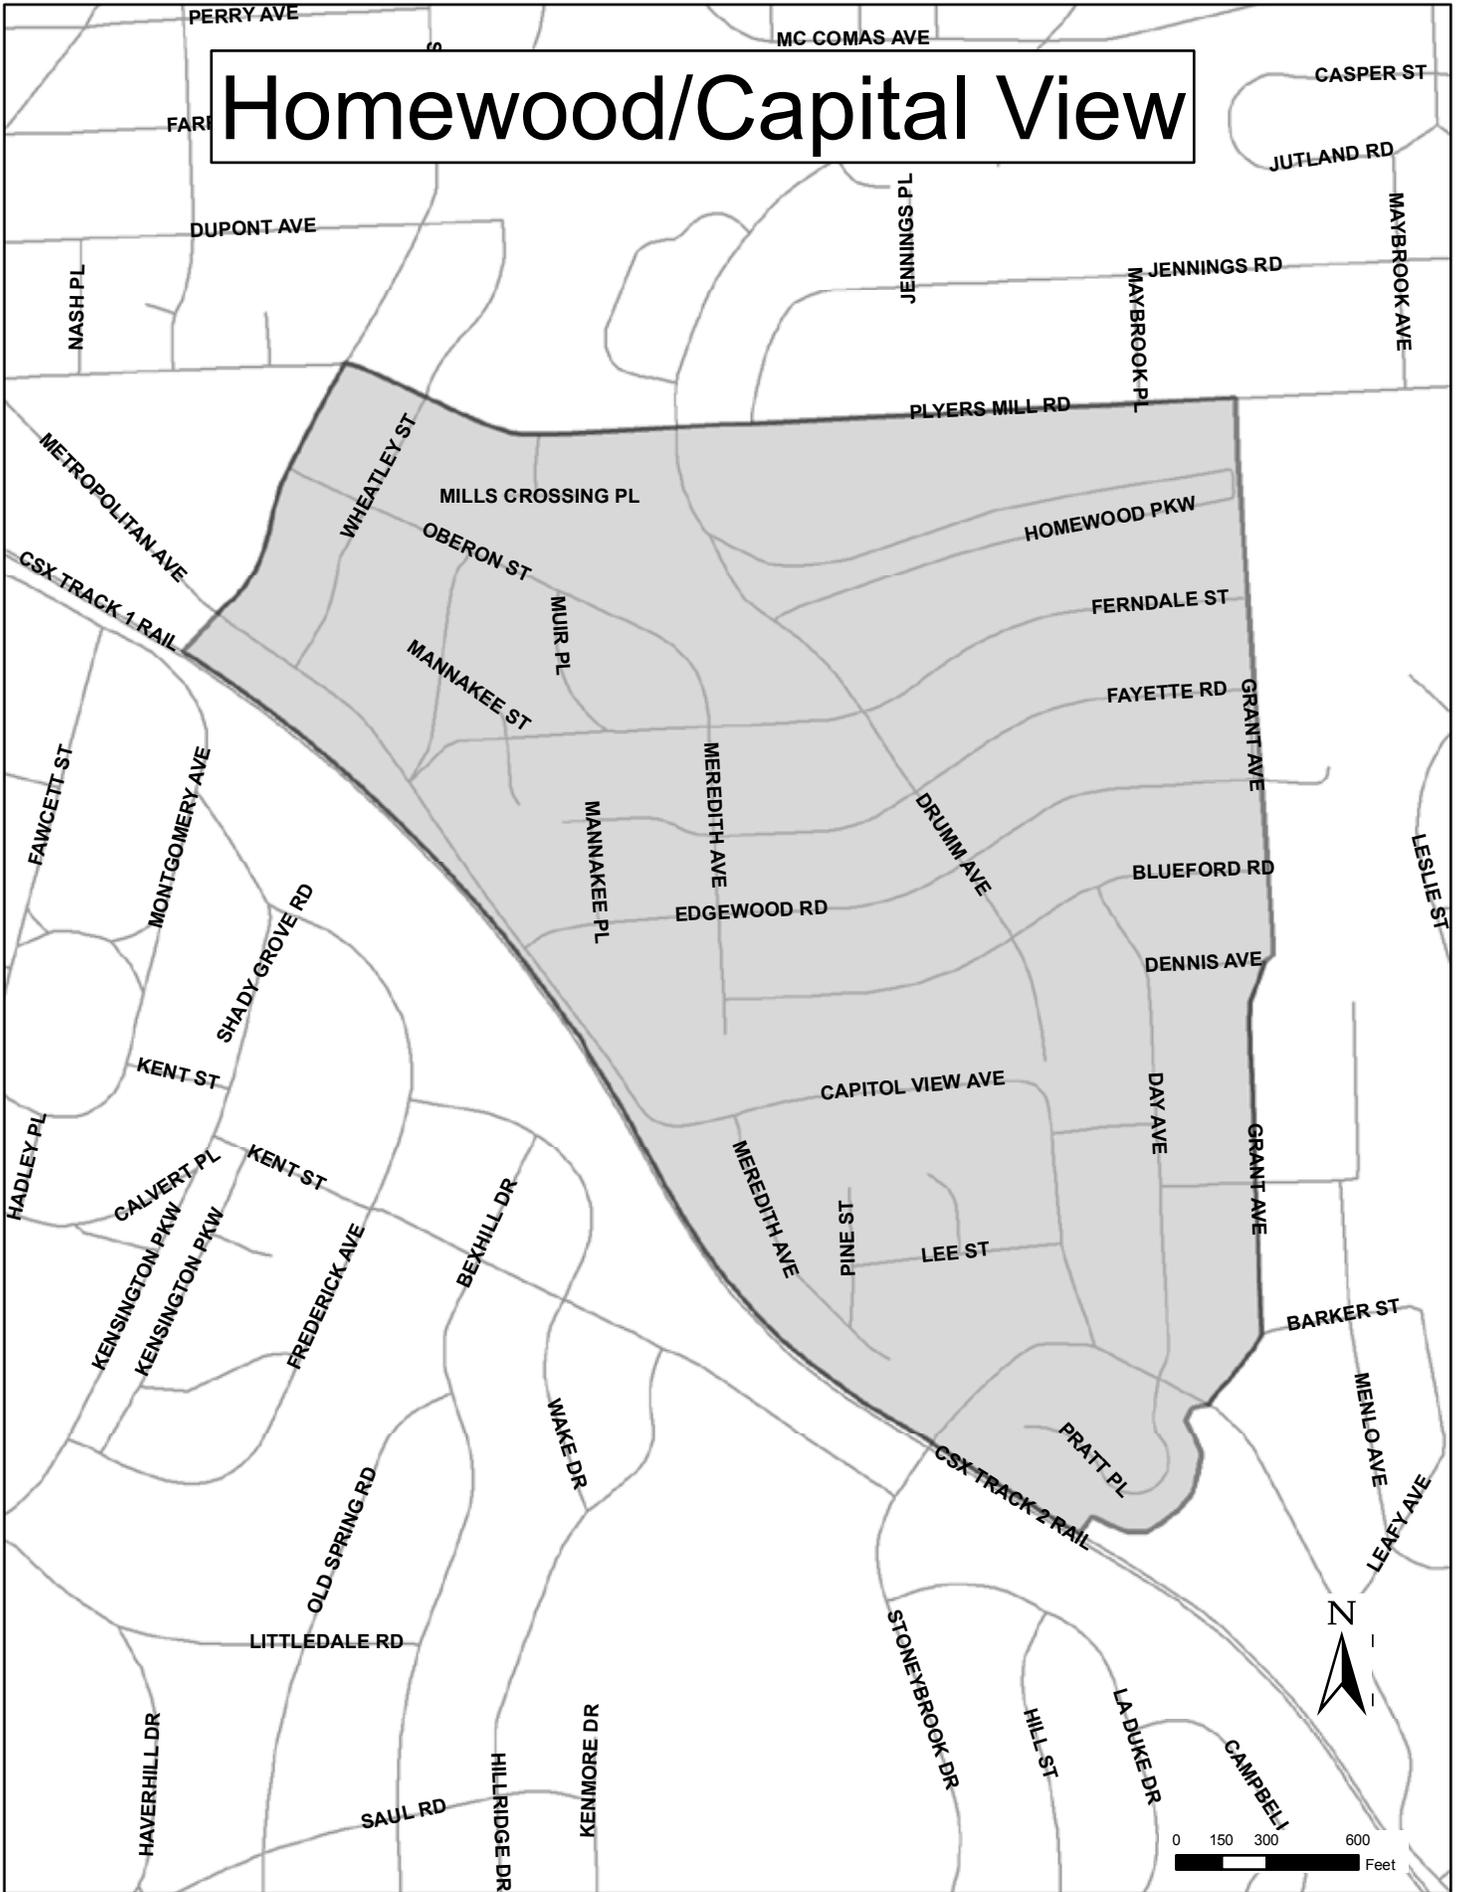


North Bethesda Grove



Woodmoor/Indian Spring Village

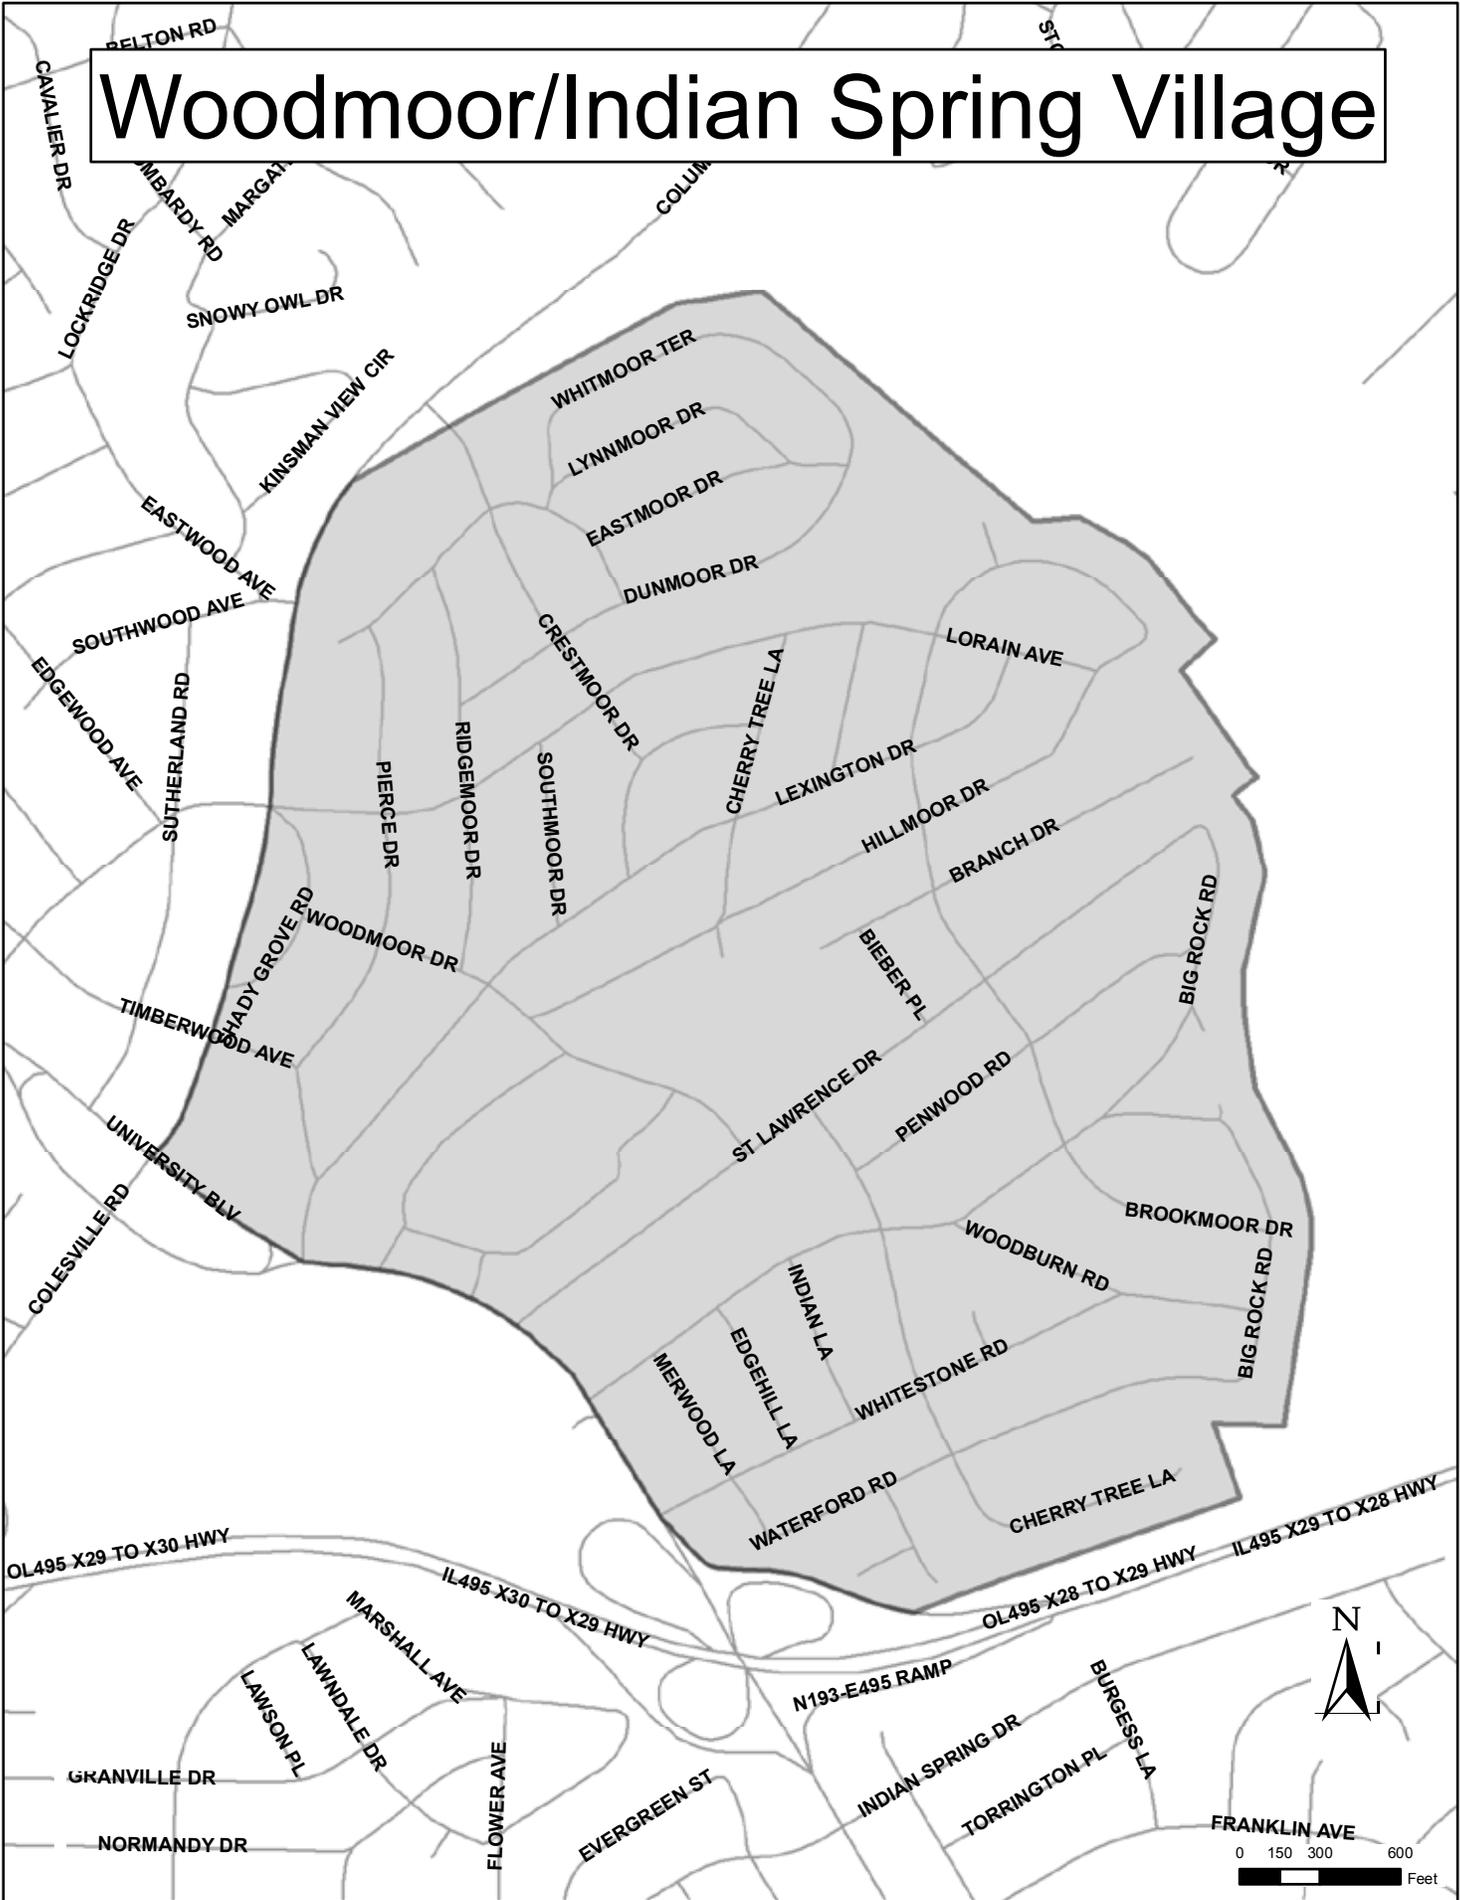





Maps of
FY04
RENEW MONTGOMERY
NEIGHBORHOODS

*Maps produced by
Joseph Pospisil
Division of Traffic Engineering and Operations
Department of Transportation*

Woodside Park East

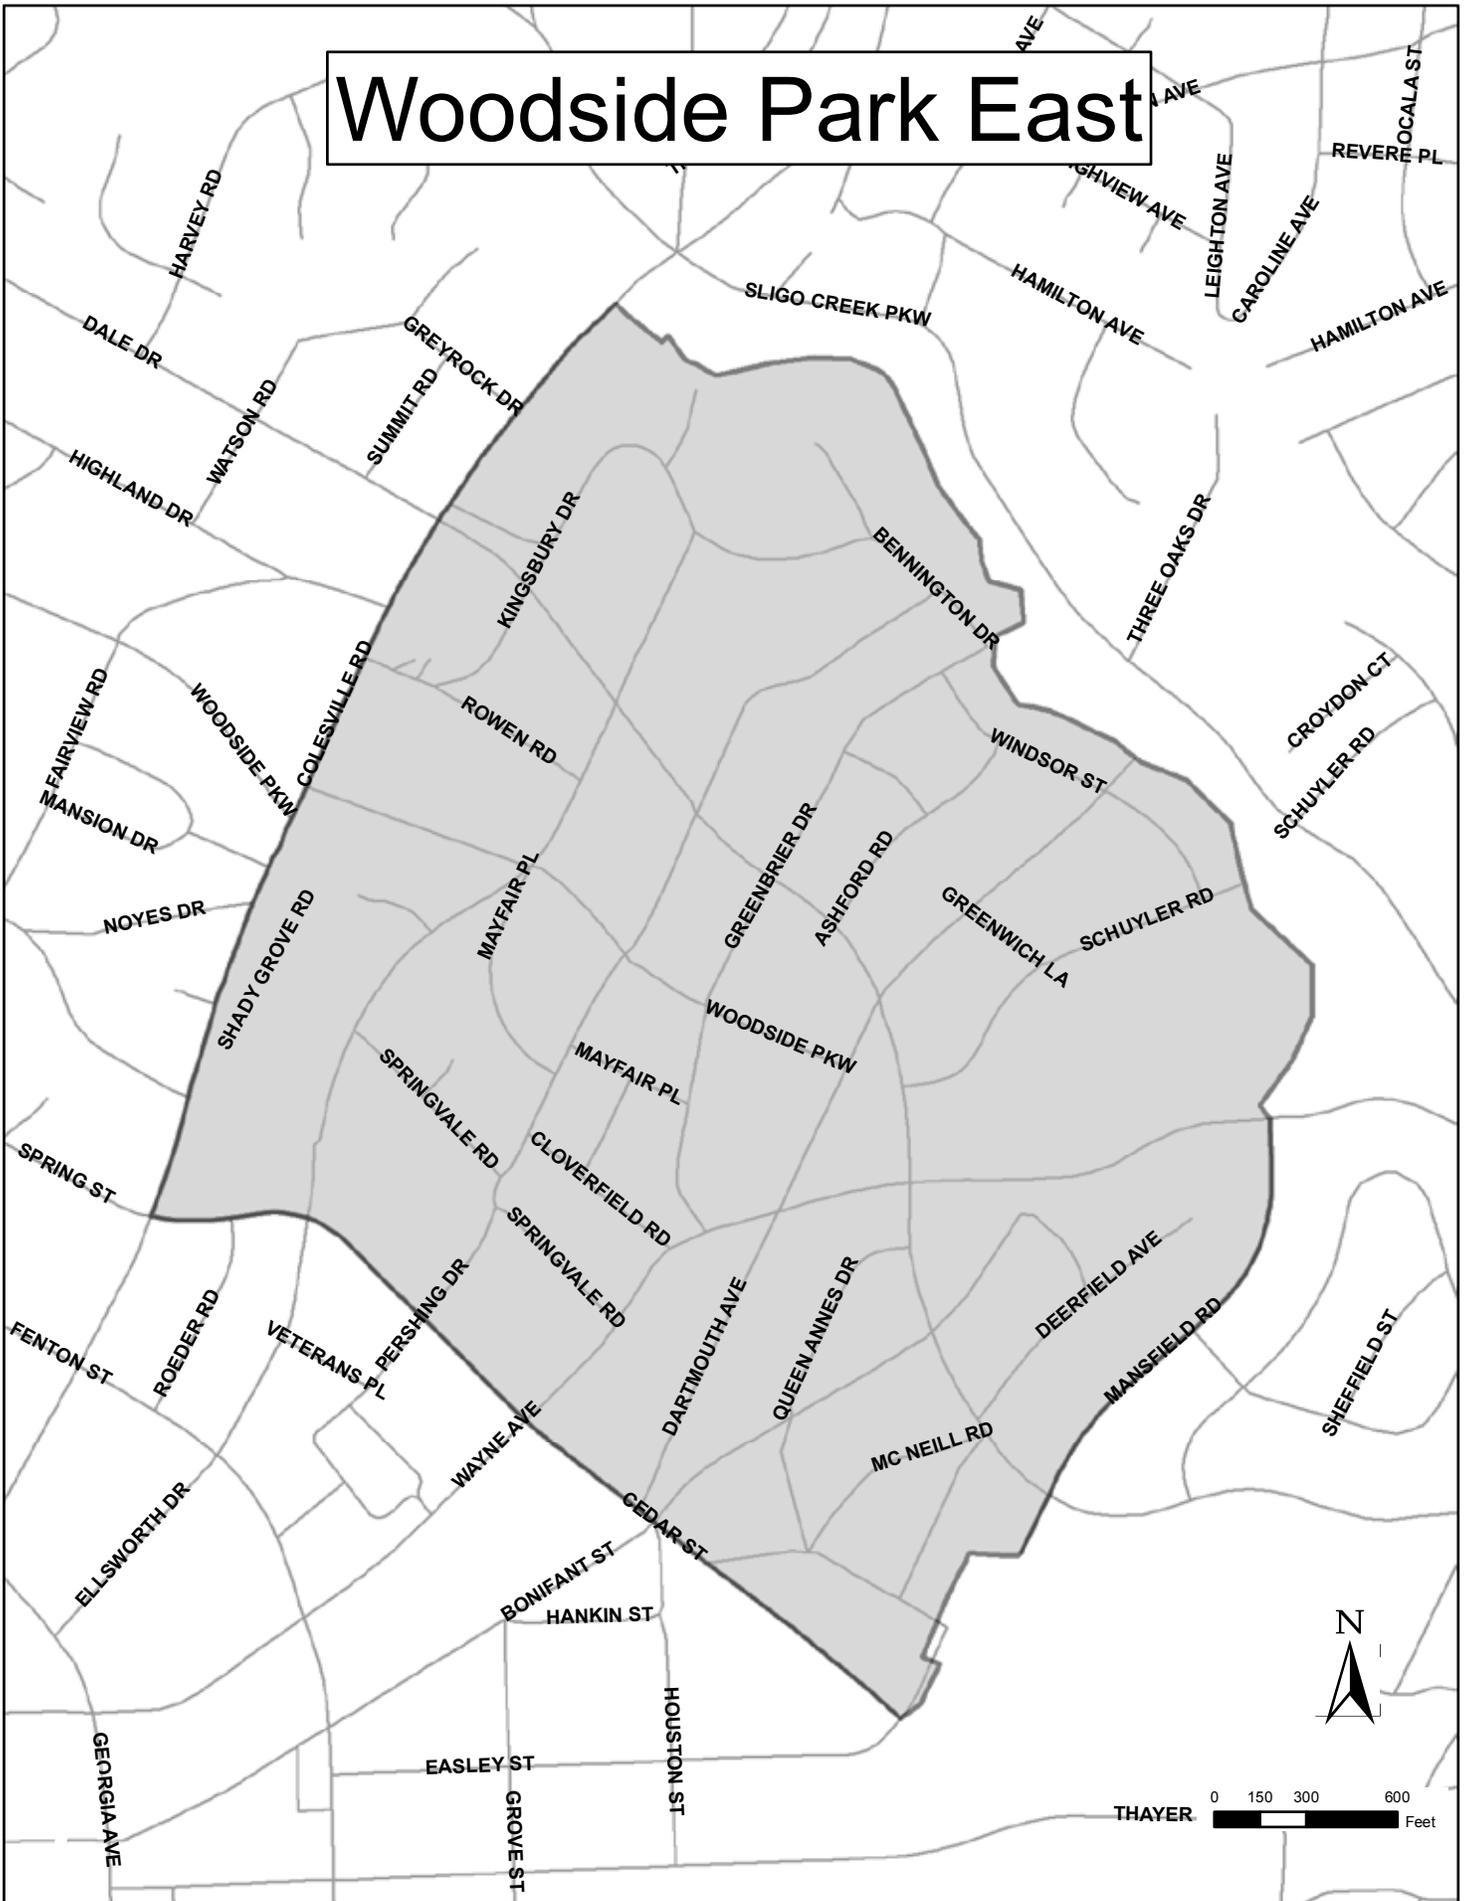



Maps of


FY05

**RENEW MONTGOMERY
NEIGHBORHOODS**


*Maps produced by
Joseph Pospisil*

*Division of Traffic Engineering and Operations
Department of Transportation*

Glenview




Northwood Park

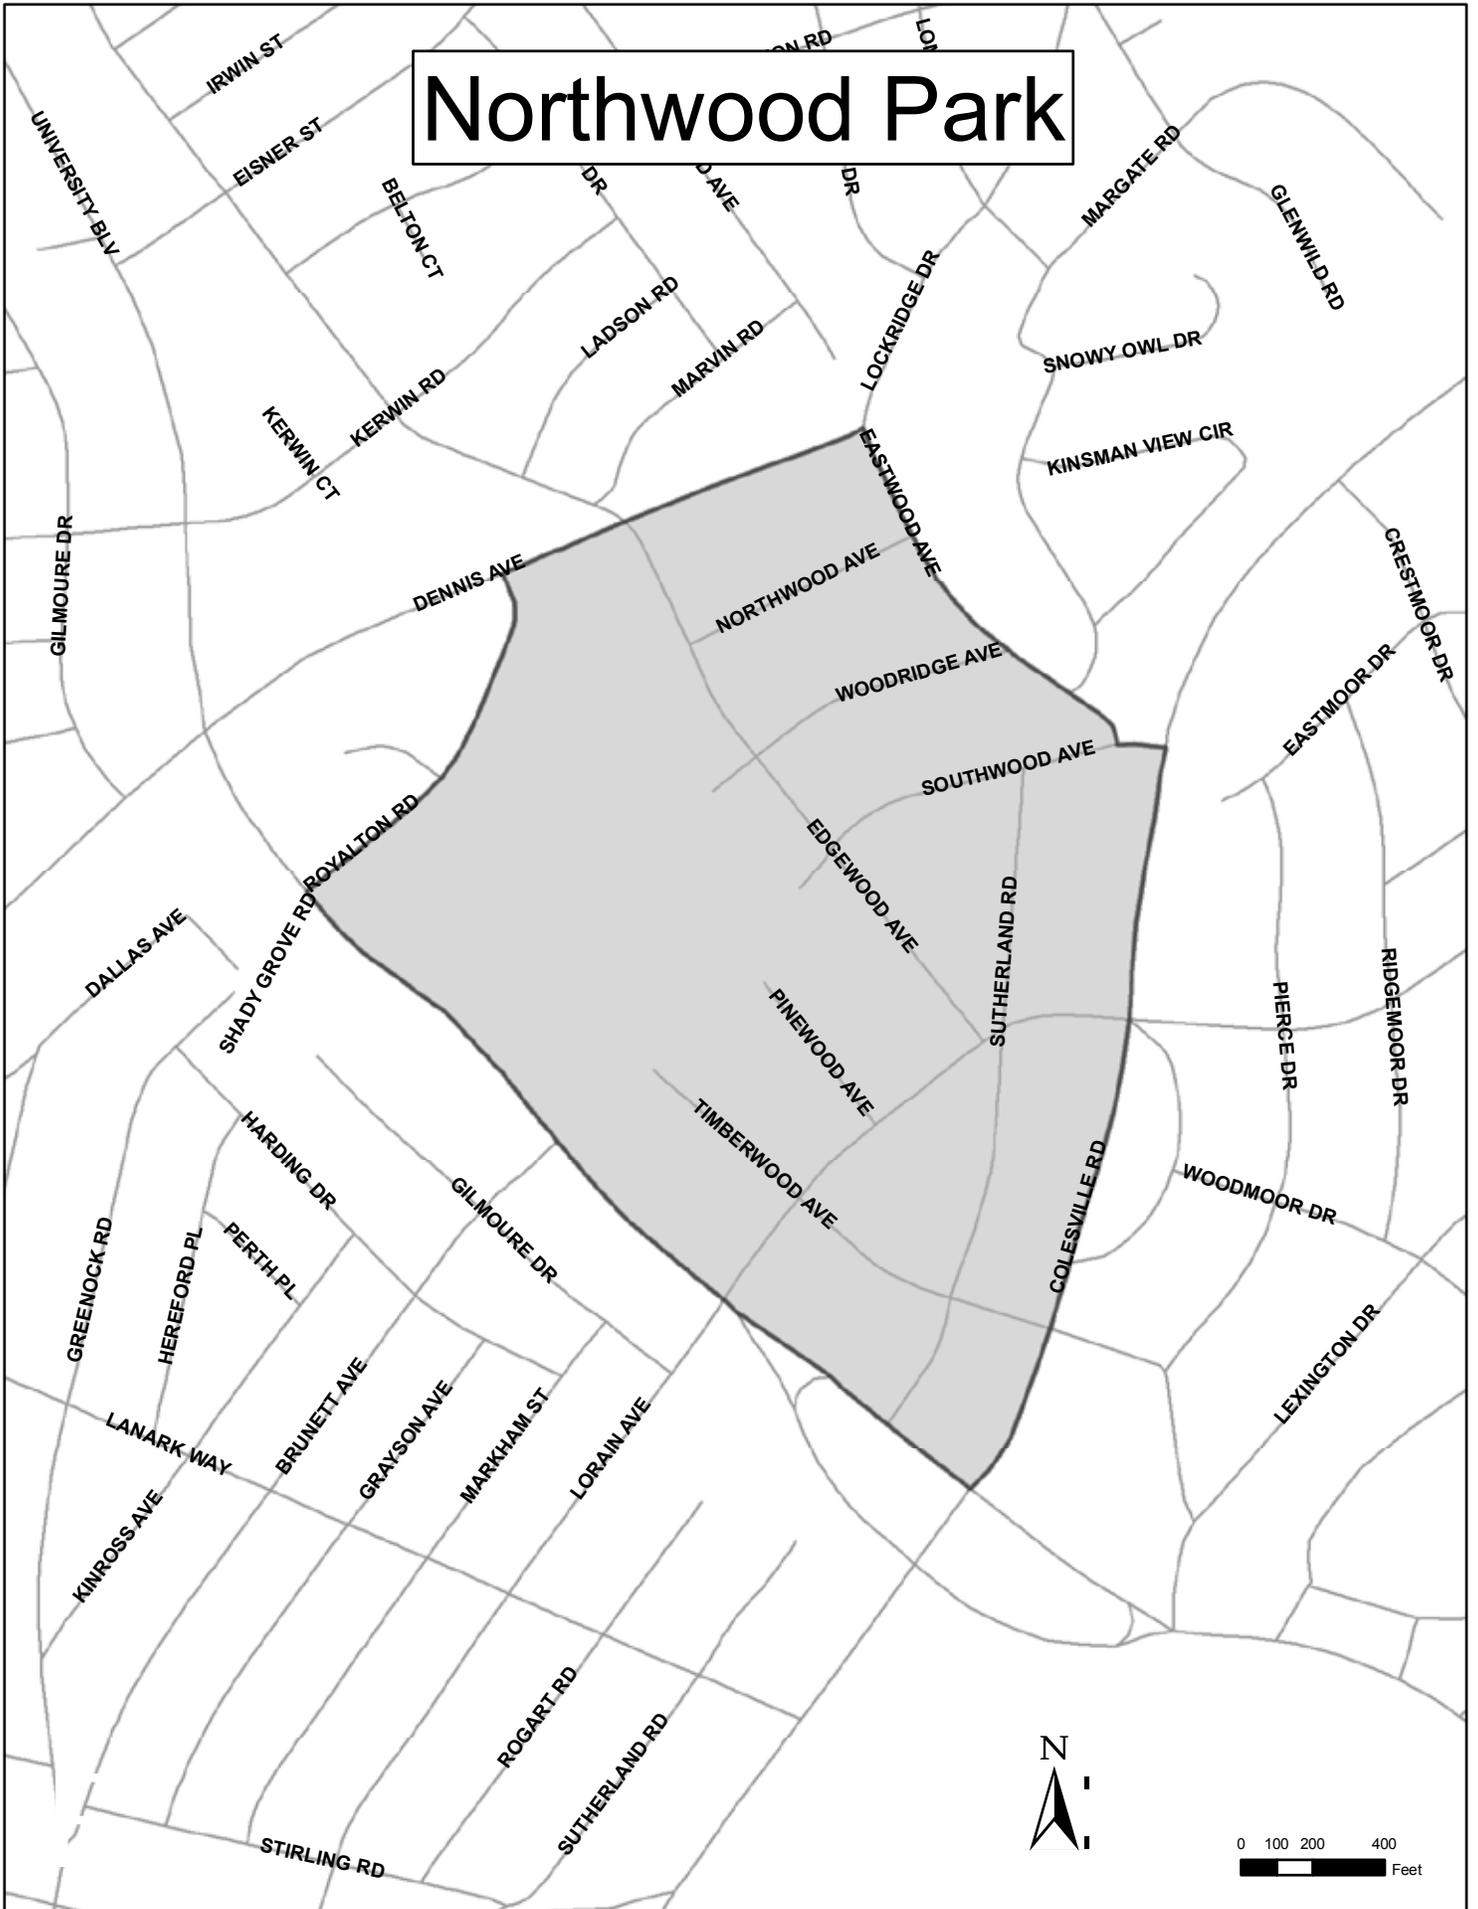

Sumner







Maps of
FY06
RENEW MONTGOMERY
NEIGHBORHOODS

*Maps produced by
Joseph Pospisil
Division of Traffic Engineering and Operations
Department of Transportation*

Glenwood/Glenbrook Knolls

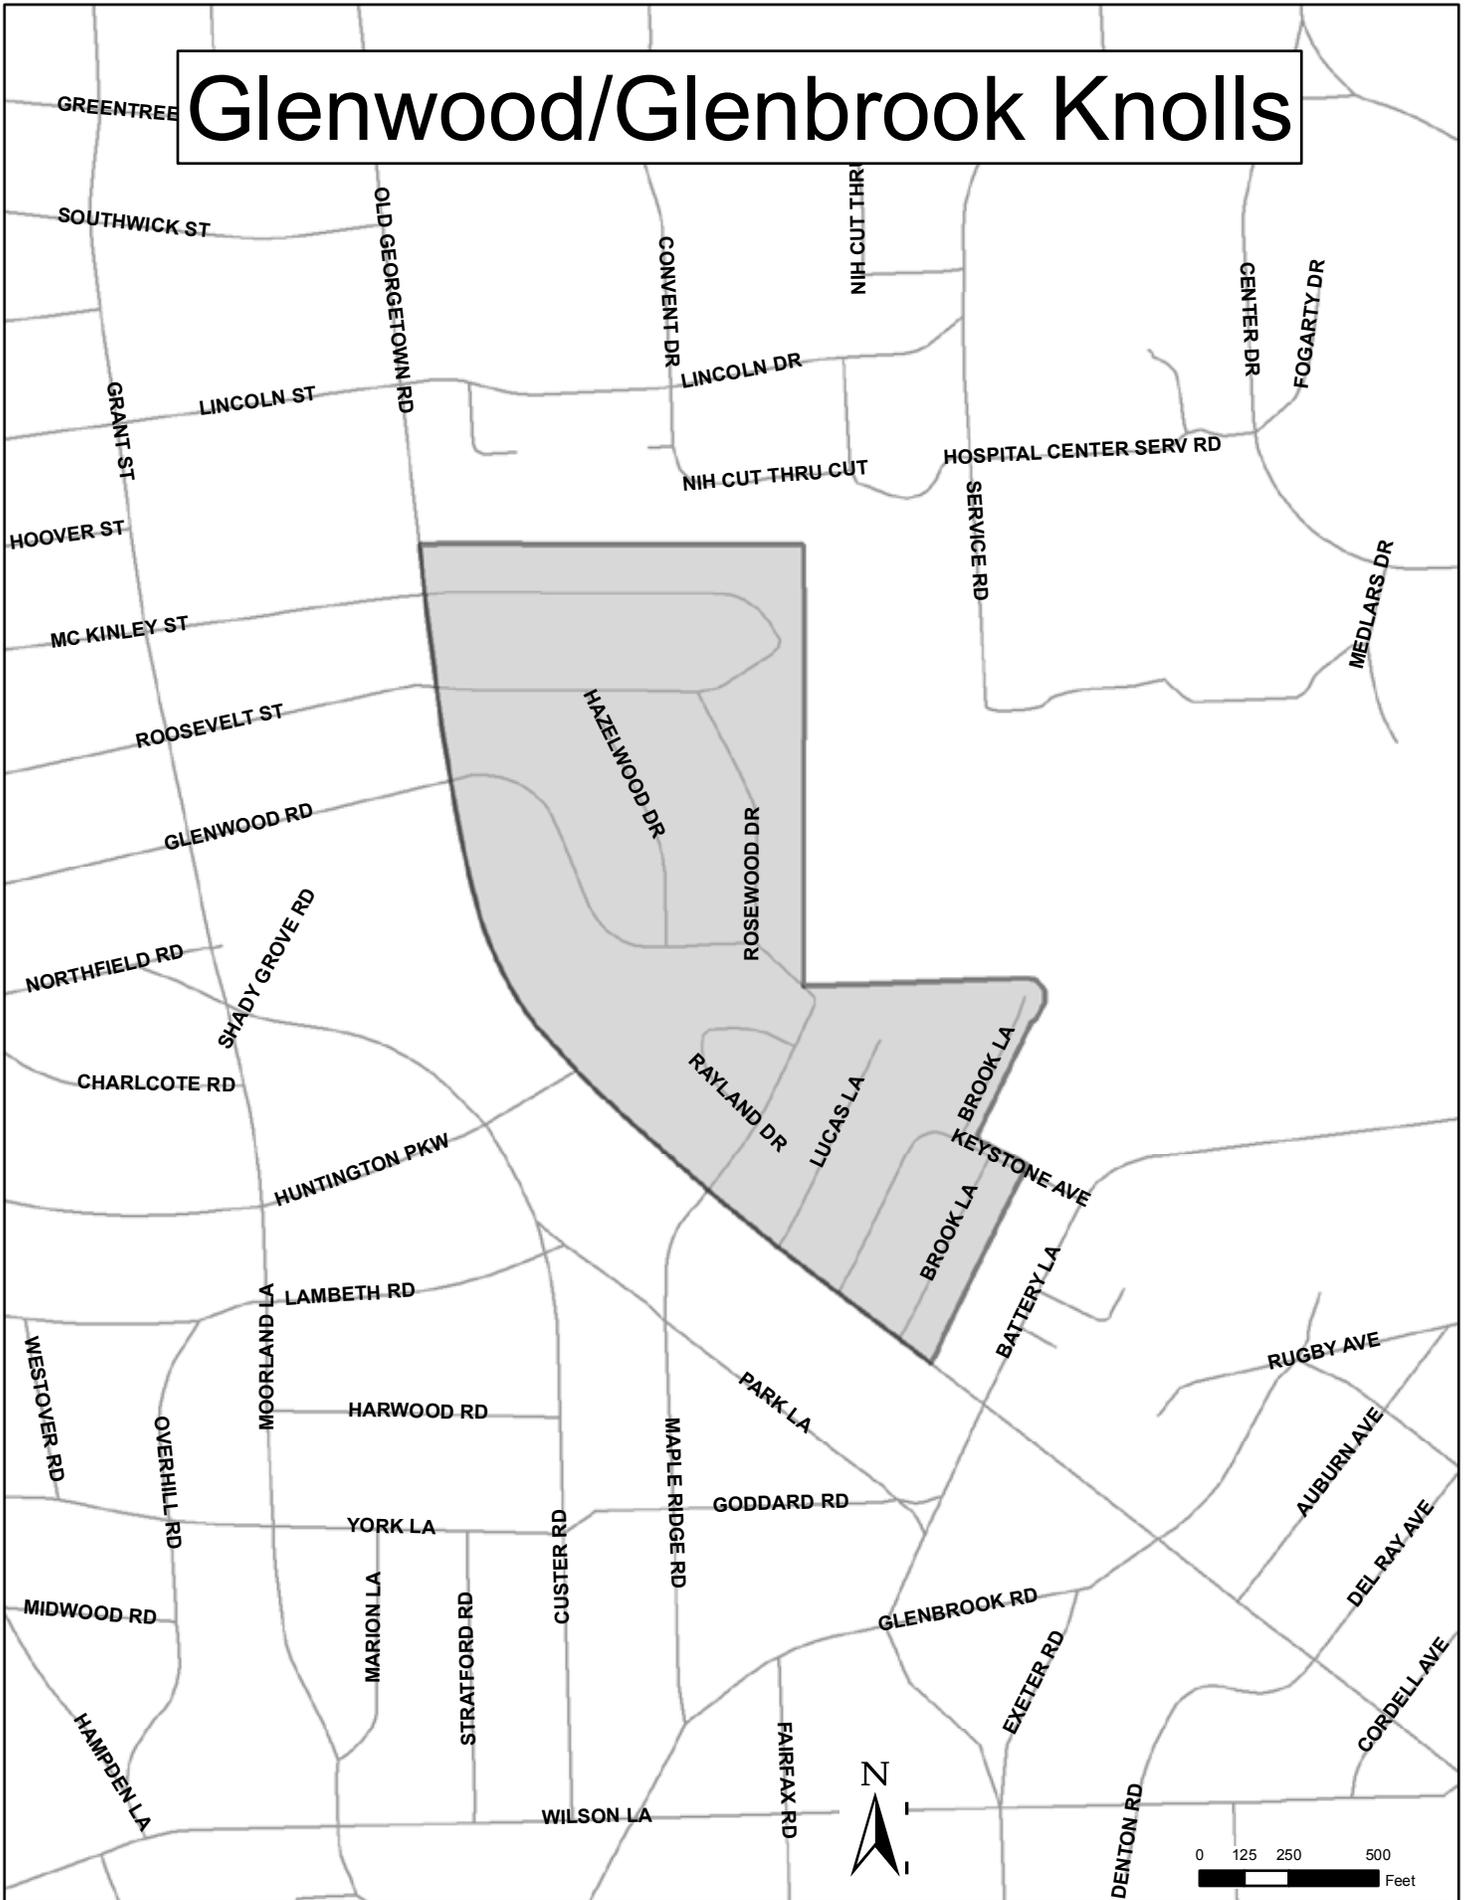


South Four Corners

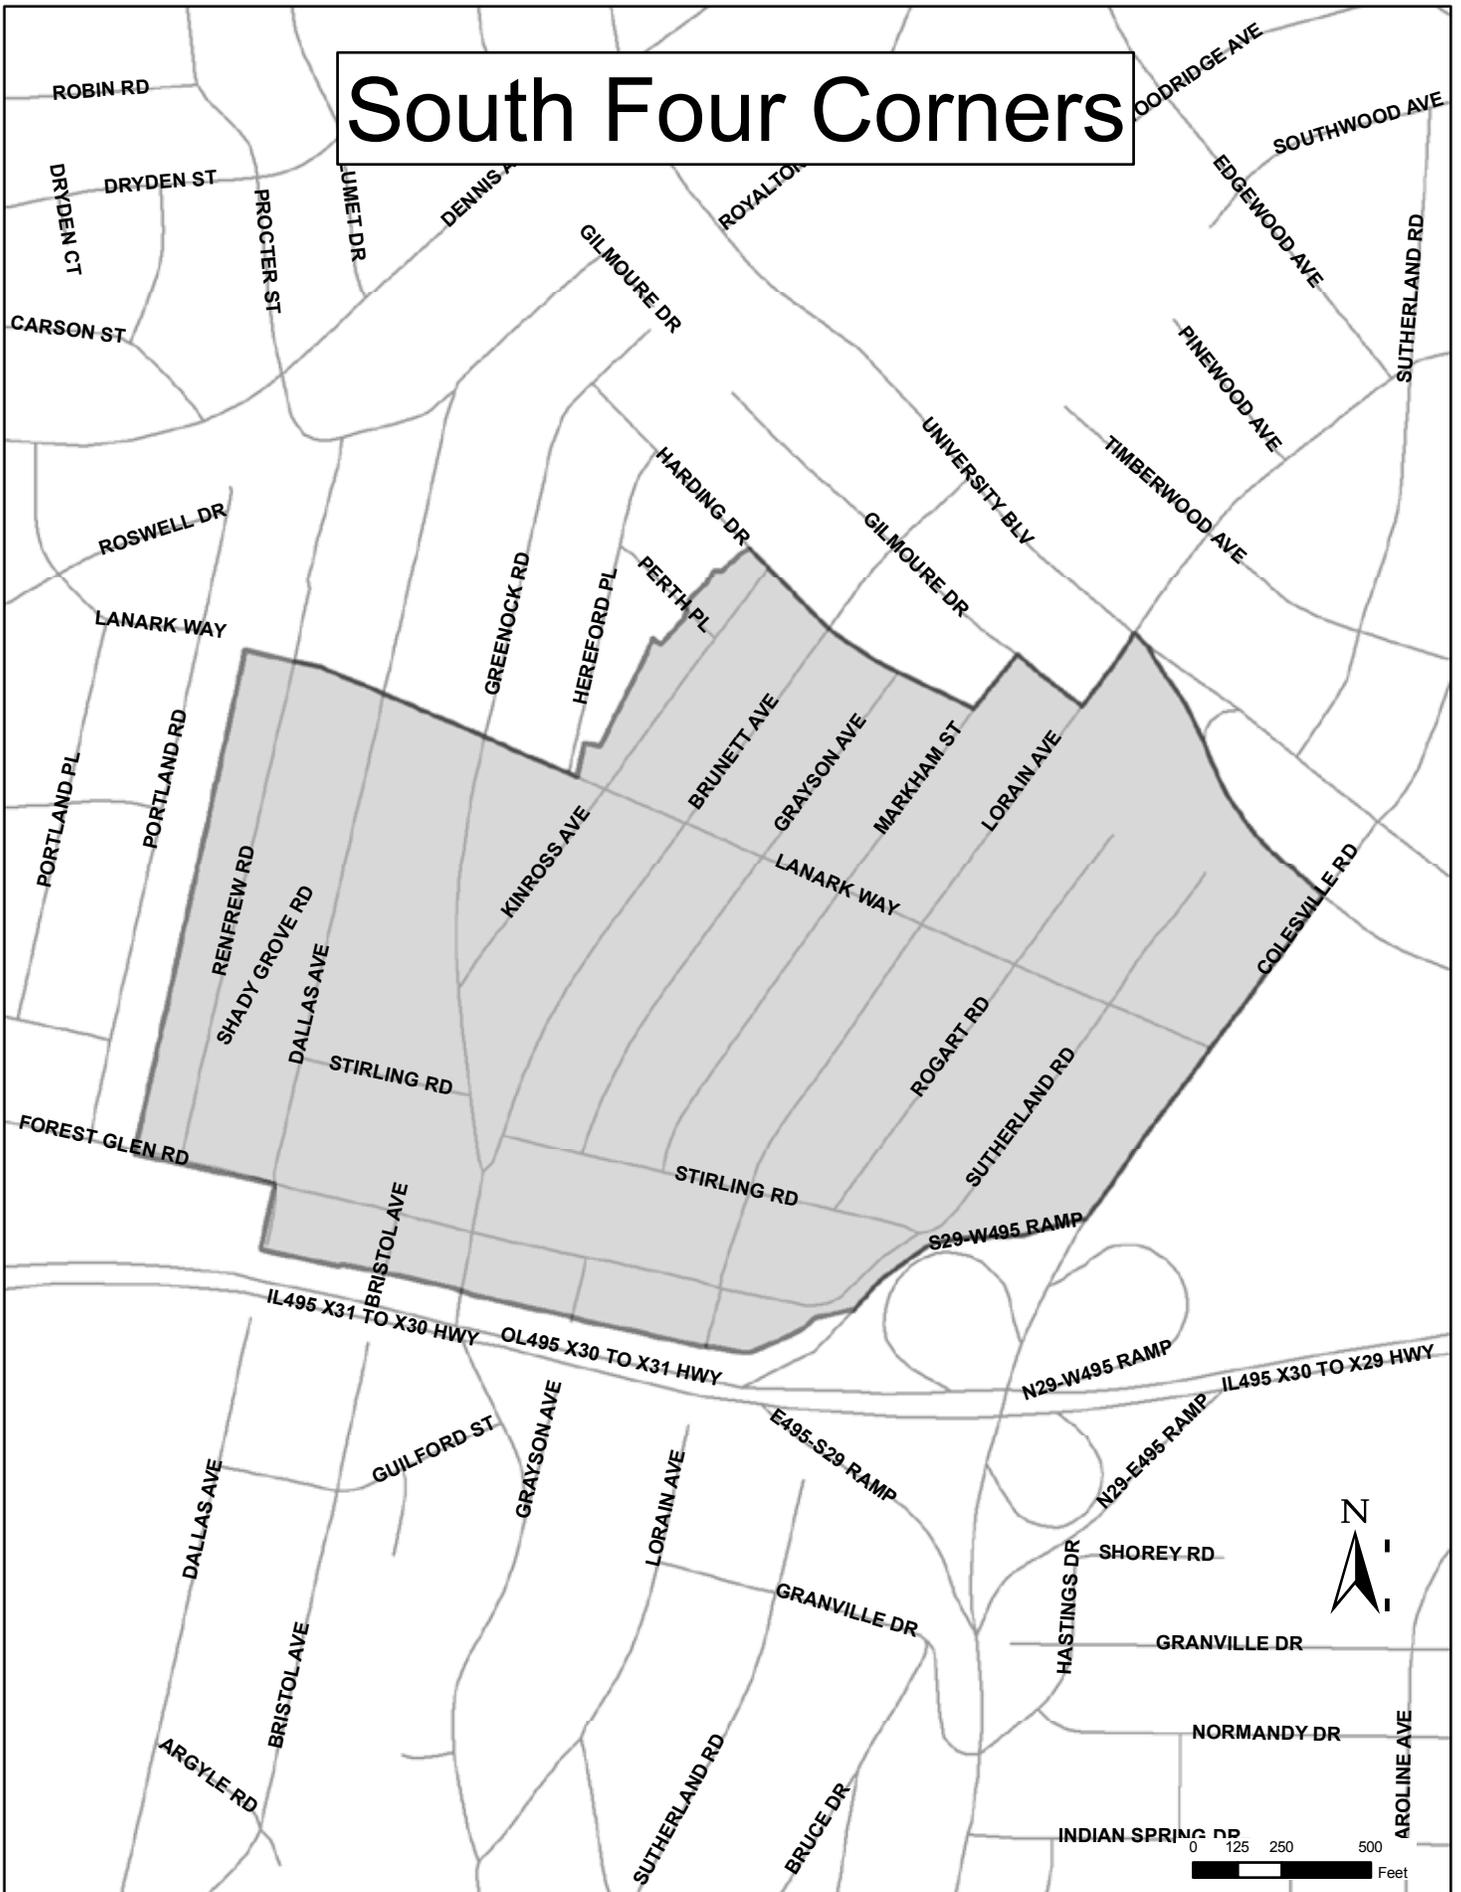

Wohlshire





Maps of

FY07


RENEW MONTGOMERY

NEIGHBORHOODS


*Maps produced by
Joseph Pospisil*

*Division of Traffic Engineering and Operations
Department of Transportation*


Carroll Knolls/Plyers Mill Estates/ Oakland Terrace

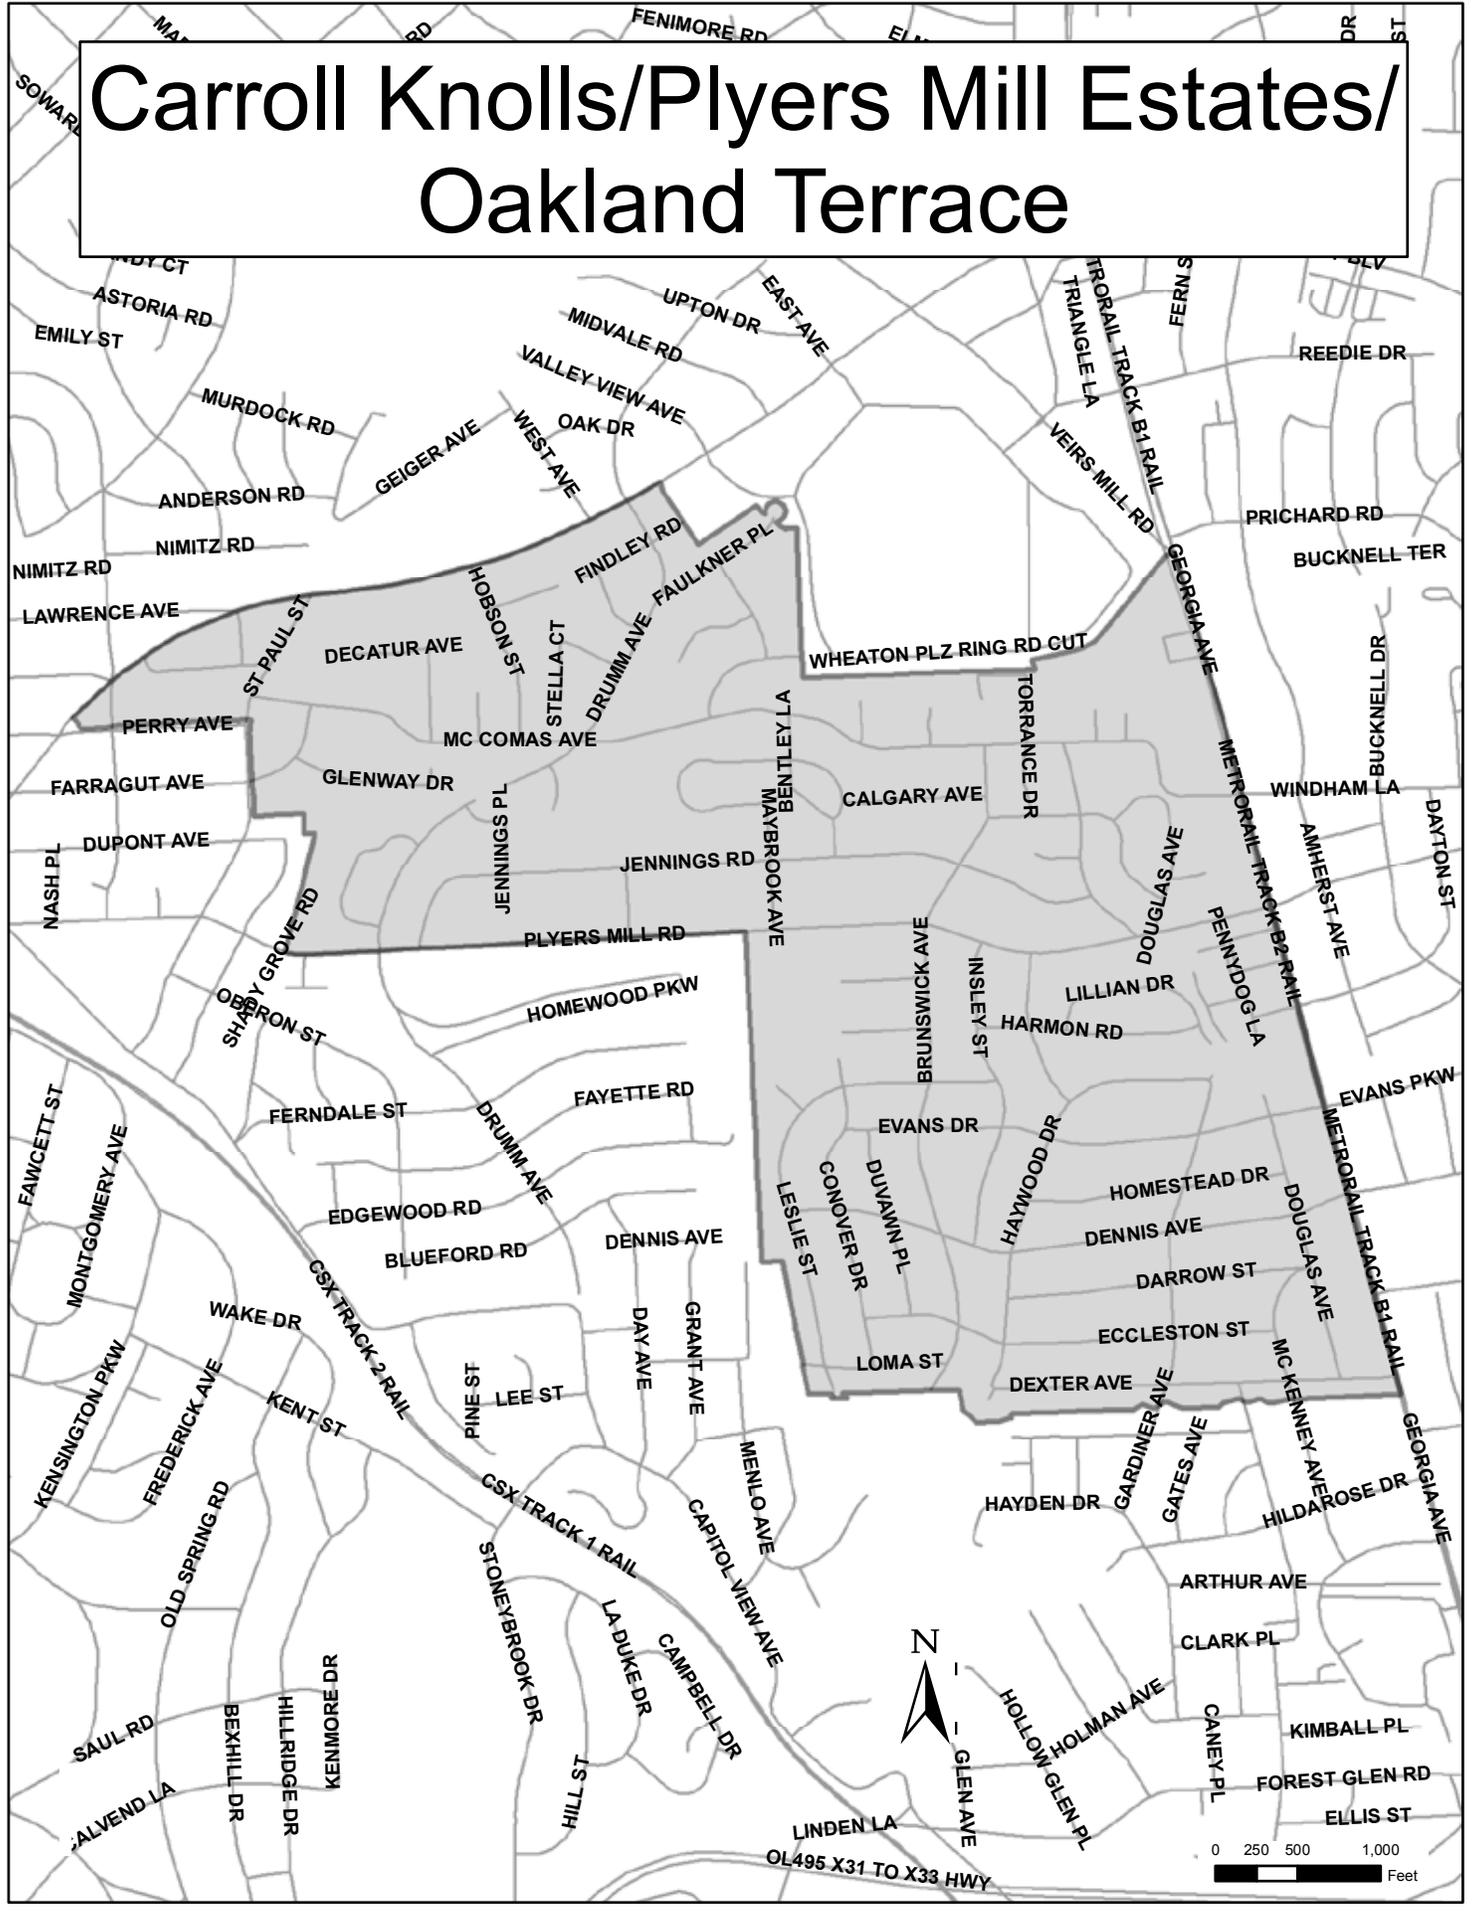


Sligo Park Knolls/Oranges/ Breewood Manor

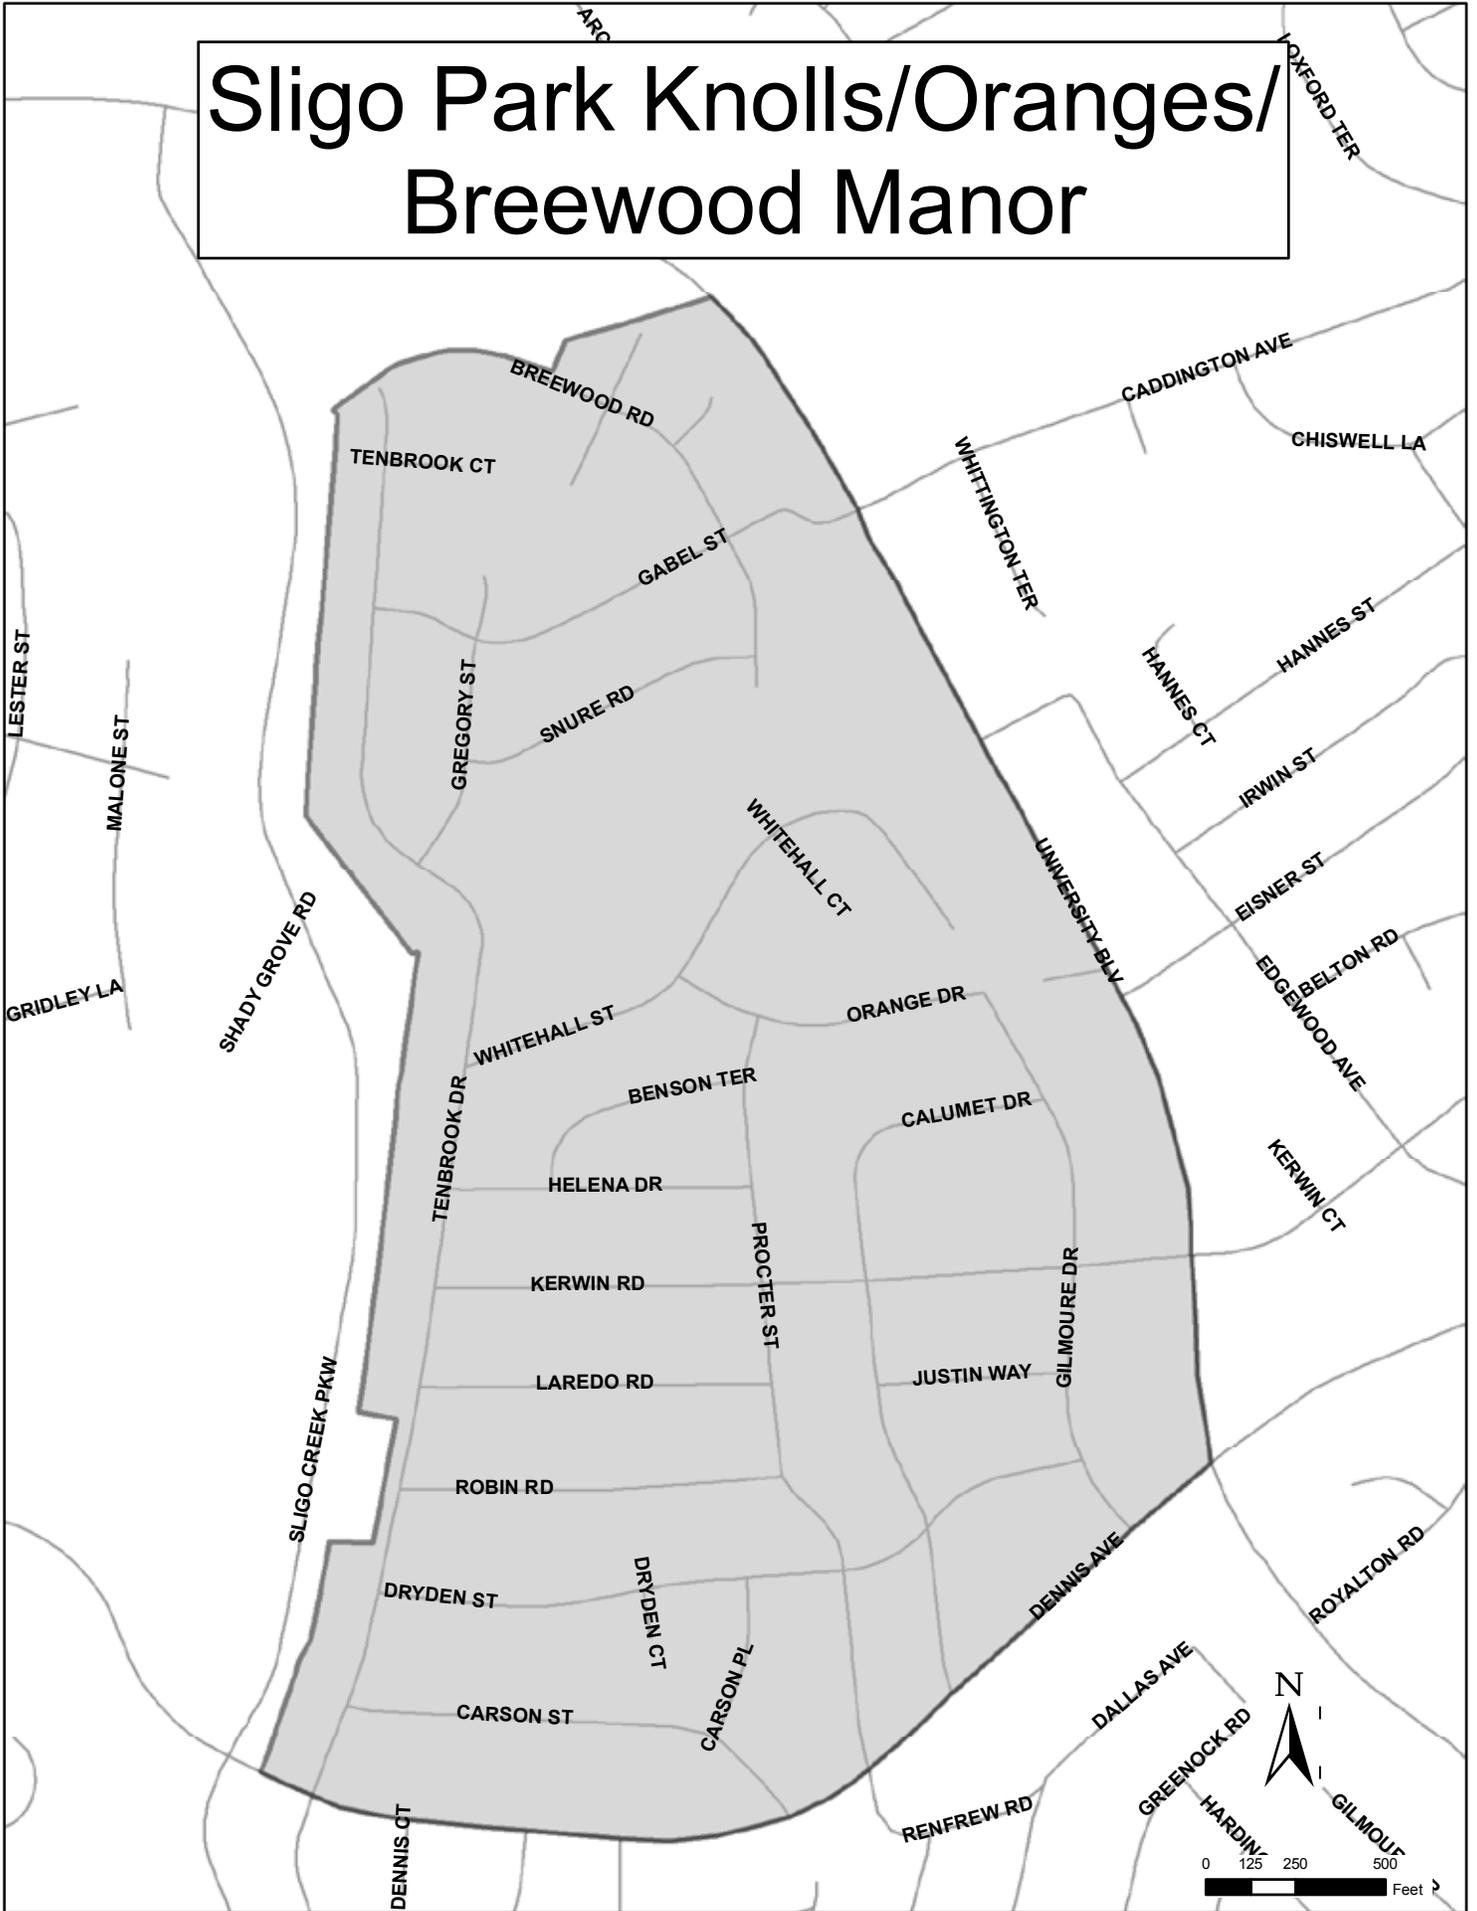

Westmoreland Hills

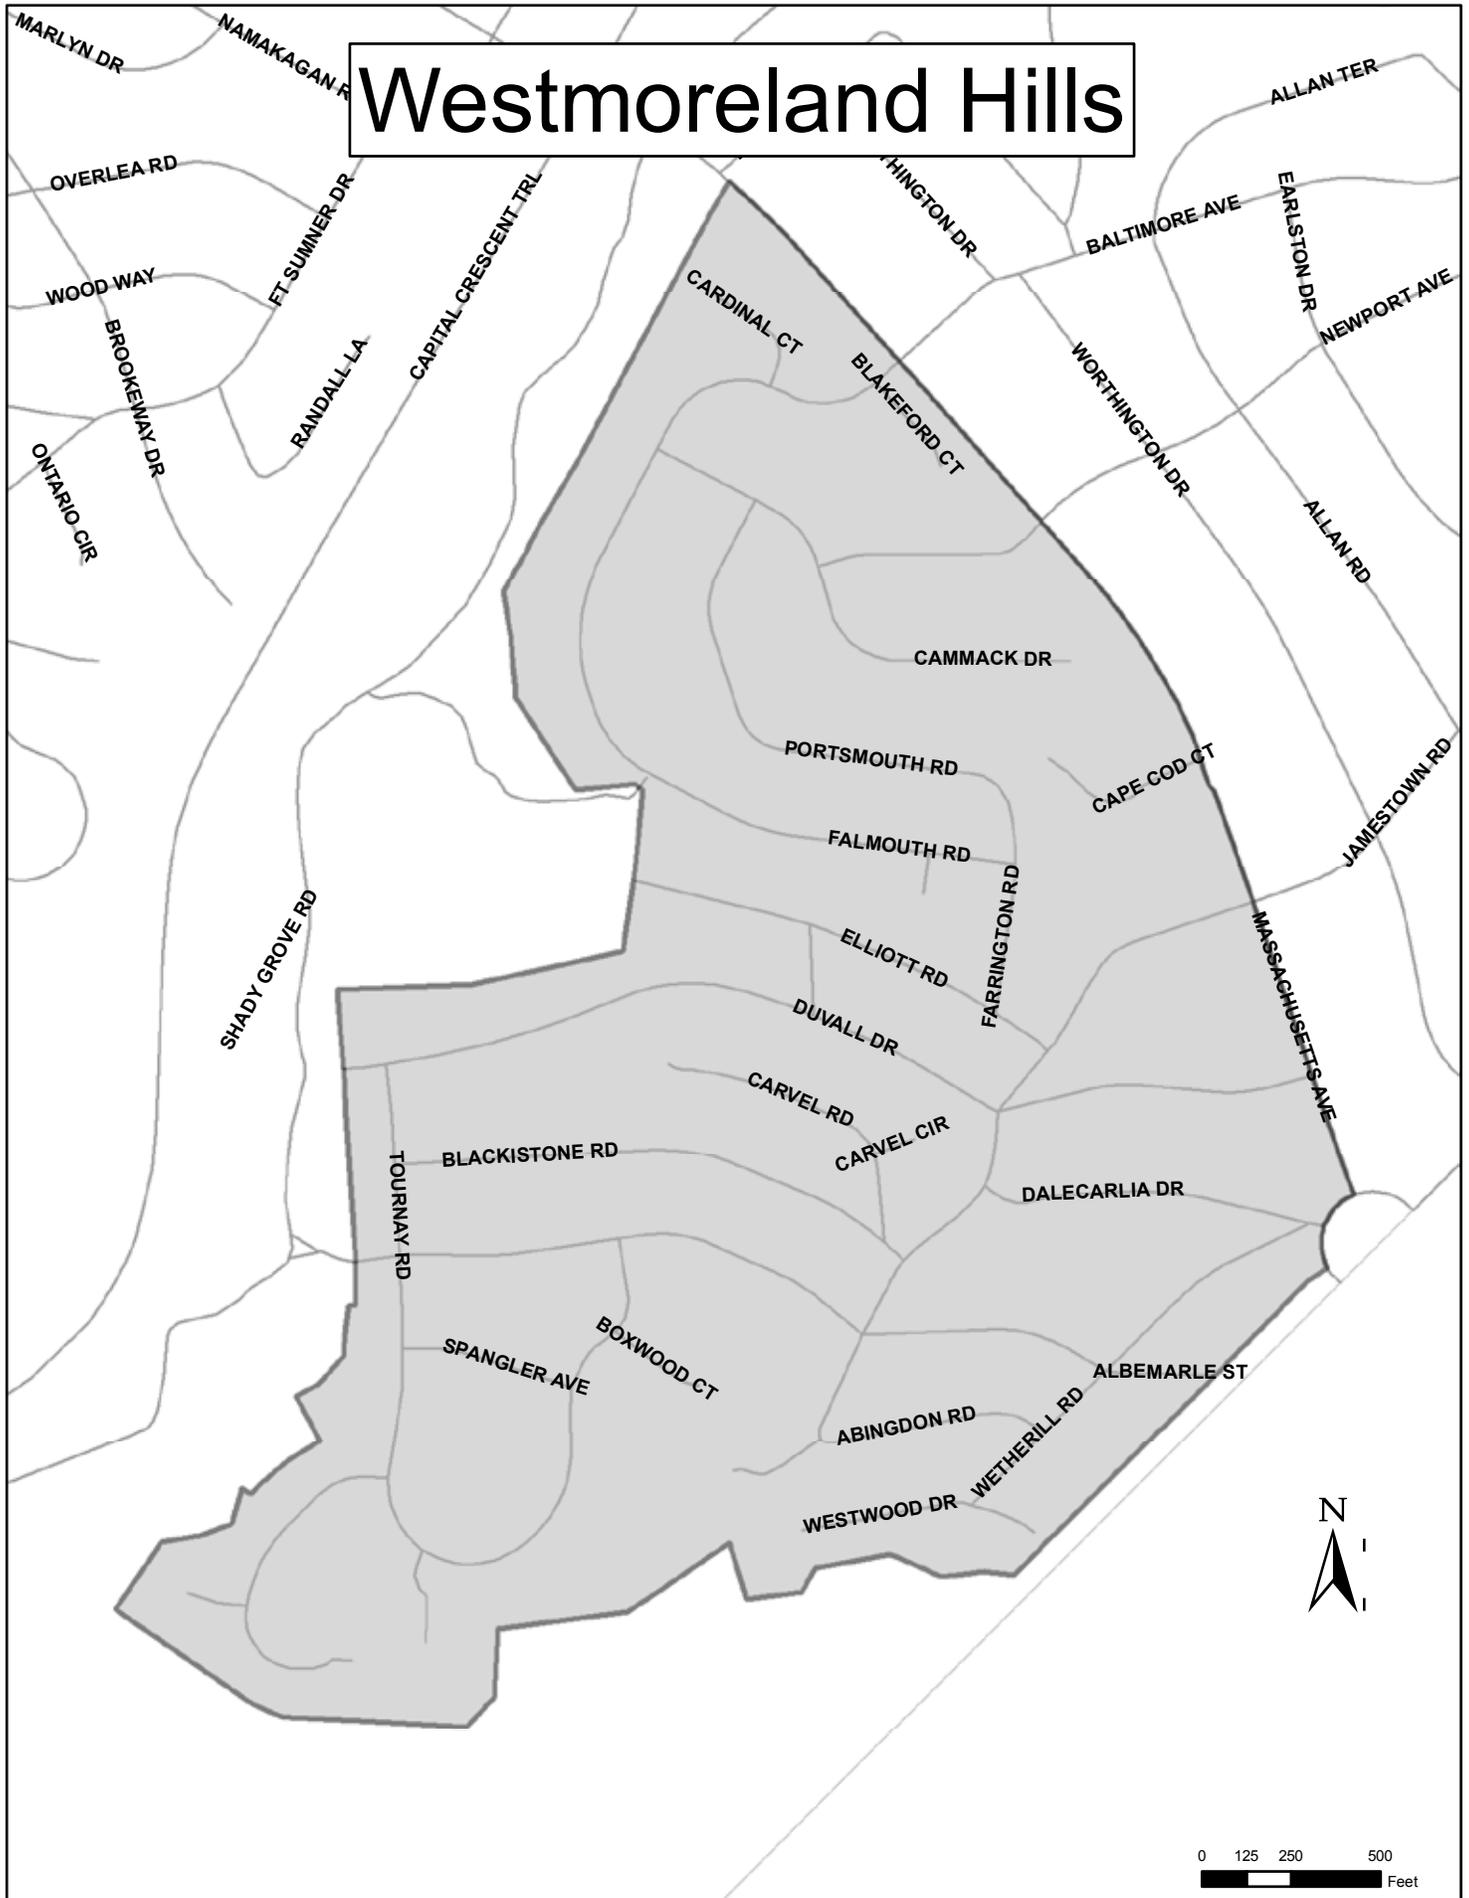




Maps of


FY08

**RENEW MONTGOMERY
NEIGHBORHOODS**

*Maps produced by
Joseph Pospisil
Division of Traffic Engineering and Operations
Department of Transportation*

Garrett Park

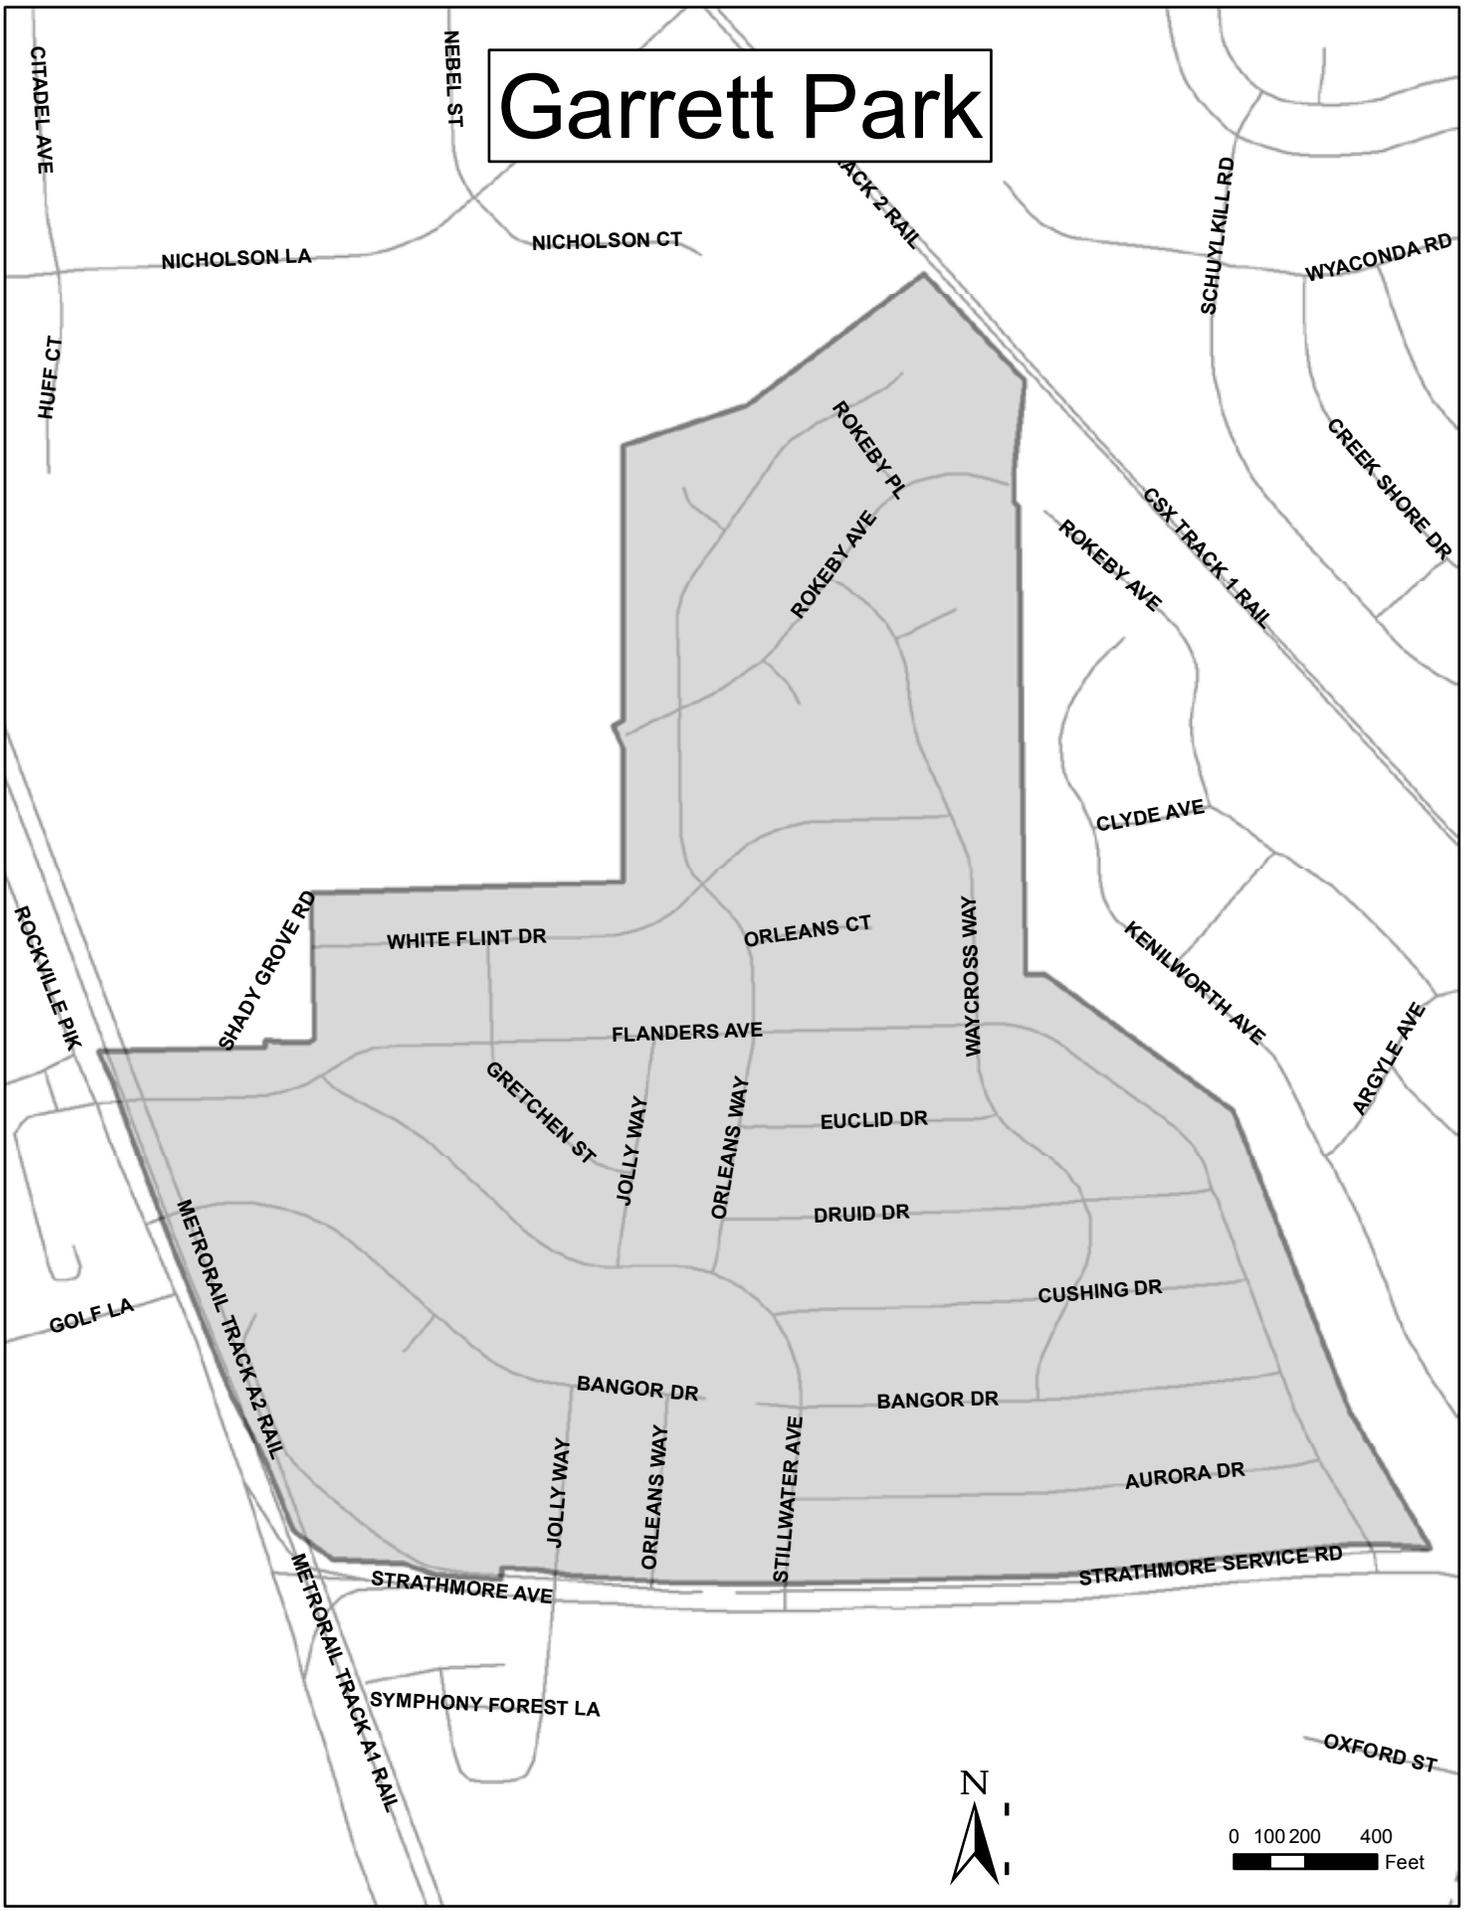




Maps of
FY09
RENEW MONTGOMERY
NEIGHBORHOODS

*Maps produced by
Joseph Pospisil
Division of Traffic Engineering and Operations
Department of Transportation*

Wheaton Woods





Maps of

FY12

**RENEW MONTGOMERY
NEIGHBORHOODS**

*Maps produced by
Joseph Pospisil*

*Division of Traffic Engineering and Operations
Department of Transportation*

Kingswell/Glenmont Forest



CONCLUSION

The Montgomery County, Maryland Department of Transportation continues to address a compelling need for infrastructure repair work through *Renew Montgomery* and ongoing efforts in other neighborhoods. As more funds are spent for *Renew Montgomery*, the rate of increase of infrastructure backlog is diminishing. The department is able to be more proactive with scheduled work rather than responding to emergency situations. *Renew Montgomery* plays an important role in improving the aesthetics and value of a neighborhood and enhancing the quality of life enjoyed by our residents.

Renewing Montgomery ...



Upgrading
and
Improving
Bus Stops

Before



After




MCDOT's Website: montgomerycountymd.gov/mcdot

MCDOT's Customer Service Center: 311


MCDOT's Transit Information Center: 311

This report published by Community Outreach, Office of the Director
June 2013



www.montgomerycountymd.gov/311

For calls made outside of Montgomery County: 240-777-0311
301-251-4850 TTY



For additional copies, write mcdot.outreach@montgomerycountymd.gov
or call 240.777.7155



"Our Partners in Delivering Excellence"

